KONN3CT EDGE

DEVELOPMENT, OPERATIONAL, COMMERCIAL AND MARKETING EXECUTION ENVIRONMENT

CONNECTION FREEDOM BY DESIGN

Executed Through the Newwaves Project Management Execution Control System

MASTER STRATEGY & EXECUTION DOCUMENT

Figure C1 | Cover Strategic Visual

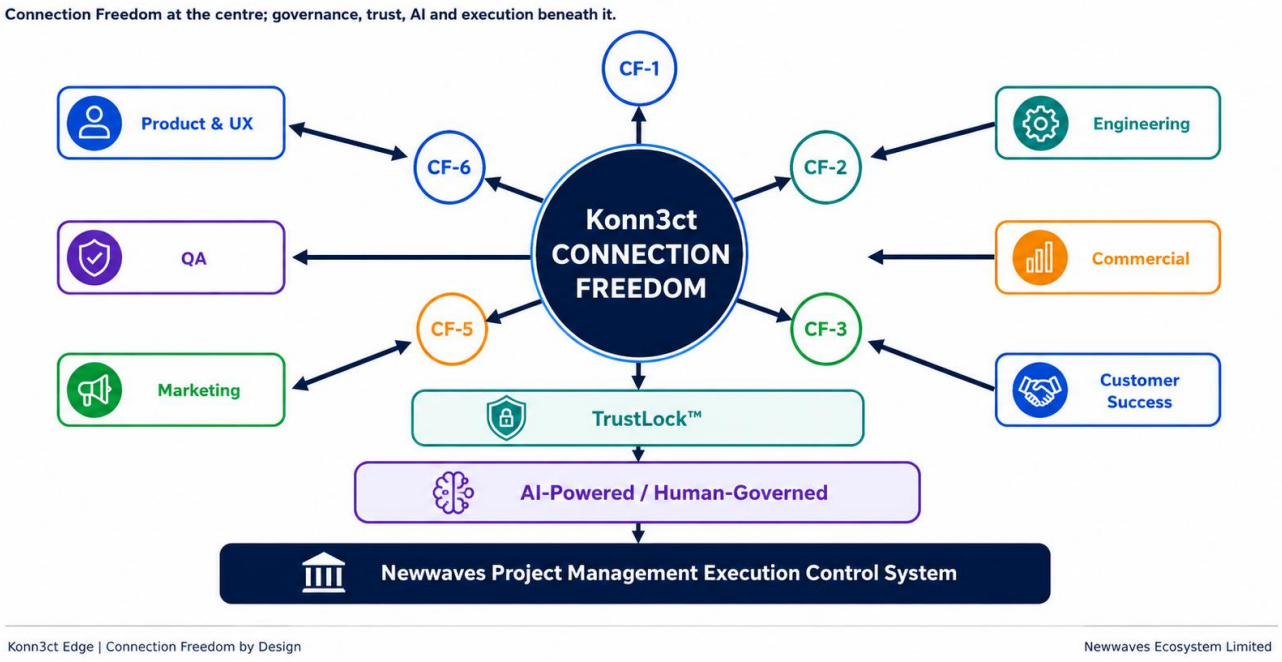


Figure C1. Cover Strategic Visual. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

Newwaves Ecosystem Limited | Version 1.0 | 10 August 2026

Document Control and Authority

Field	Approved Value
Document Title	Konn3ct Edge Development, Operational, Commercial and Marketing Execution Environment
Strategic Doctrine	Connection Freedom by Design
Execution System	Newwaves Project Management Execution Control System (Odoo 19 Enterprise)
Programme Start	10 August 2026
Day-30 Gate	8 September 2026
Day-90 Gate	7 November 2026
Year-1 Marketing Horizon	10 August 2026 – 9 August 2027
Initial Blueprint Completion Target	31 January 2028
Executive Sponsor	Chief Executive Officer, Newwaves Ecosystem Limited
Primary Delivery Managers	Growth & Ecosystem Manager; Technology & Business Operations Manager
Document Status	Master Strategy and Execution Reference
Review Rhythm	Weekly operational review; monthly strategic review; quarterly strategy refresh
Strategy Partner Rule	ChatGPT should treat this approved document as the principal strategic reference unless superseded by a formally approved newer decision in Odoo.

Authority Rule

This document is the strategic baseline. Weekly execution changes should normally be recorded in Odoo rather than by constantly rewriting the strategy. Material changes to Blueprint direction, Connection Freedom doctrine, major architecture, commercial model, Day-90 commitments or roadmap require documented approval.

Table of Contents

A static Table of Contents is inserted in the final file for navigation. Headings are also formatted with Word heading styles for further editing and automatic TOC generation if preferred.

Document Control and Authority
1. Executive Summary
    1.1 Non-Negotiable Outcomes
2. Current-State Reality and Starting Assets
    2.1 1Gov Version 1 — Protected Production and Customer Reference
    2.2 New Konn3ct Version 1 — Current Product and Market Baseline
    2.3 Konn3ct Edge — Progressive Transformation
    2.4 Retain–Stabilise–Converge Decision Model
3. Connection Freedom by Design
    3.1 Experience Principles
    3.2 Connection Freedom Index (CFI)
4. Organisation, Governance and Decision Rights
    4.1 CEO and Two-Manager Operating Model

4.2 Key Governance Bodies
4.3 QA Independence
5. Newwaves Project Management Execution Control System
5.1 Core Odoo Data Model
5.2 End-to-End Lifecycle
5.3 Weekly Sub-Sprint Operating Unit
5.4 Weekly Sprint Score
5.5 Weekly Management Rhythm
6. First 30 Days — PM and Integration Go-Live
6.1 Day-30 Acceptance Test
7. Tool Architecture, Systems of Record and Integrations
7.1 Systems of Record
7.2 Integration Principles
8. ChatGPT as Strategy Partner
8.1 Strategy Partner Operating Instructions
8.2 Recommended AI Workspaces
9. Antigravity and Controlled AI-Assisted Engineering
9.1 Mandatory Work-Order Fields
9.2 AI Autonomy Levels
10. Common Core, White-Label Governance and Release Management
10.1 Common-Core Rules
10.2 Release Rings
11. Blueprint-to-Release Traceability
12. First 90 Days — 13 Weekly Sub-Sprints
13. Day-90 Growth Objective — 10,000 Free / 300 Paid
13.1 Qualifying User Definitions
13.2 Run-Rate Management
13.3 Growth Command Centre
14. One-Year Connection Freedom Marketing Execution Programme
14.1 Marketing Operating Model
14.2 First 13 Weeks — Detailed Marketing Sprints
14.3 Weeks 14–52 — Weekly Marketing Sprint Calendar
15. Product and User Experience Execution
15.1 Experience-Led Prioritisation
16. Mobile Connection Freedom Programme
17. Technical Architecture and Konn3ct Edge Transformation
17.1 Target Architecture Domains
18. Kubernetes, Autoscaling and Site Reliability Engineering
18.1 Kubernetes Implementation Sequence
18.2 Autoscaling Signals
18.3 SRE Targets
19. DevOps, DevSecOps and CI/CD
20. Quality Assurance and Release Certification
20.1 Required Personas
21. TrustLock™, Cybersecurity, Privacy and Licensing
21.1 Security-by-Design Gates
21.2 Software Licensing and SBOM
22. Commercial Model and Revenue Operations
23. Growth, Marketing Technology and Product-Led Acquisition

23.1 Growth Blocker Triage
24. Customer Success, Support and Feedback-to-Engineering
25. Dashboards, KPIs and Management Intelligence
25.1 CEO Dashboard
25.2 Growth & Ecosystem Dashboard
25.3 Technology & Business Operations Dashboard
25.4 PMO Dashboard
26. Risk Management
27. Internal Capability and Culture Transformation
27.1 Functions to Score
28. 18-Month Blueprint Roadmap
29. Immediate Action — Monday, 10 August 2026
29.1 First 20 Management Actions
29.2 First 50 Operational Setup Tasks
30. First Two-Week Sprint and Weekly Sub-Sprints
30.1 Sprint 1 — 10–23 August 2026
30.2 Remaining 90-Day Biweekly Sprints
31. Weekly CEO Command Report Template
32. Definition of Done and Production Readiness
32.1 Production Readiness Checklist
33. Ongoing Strategy Governance and ChatGPT Review Cycle
33.1 Strategy Partner Review Questions
34. Newwaves Konn3ct Edge Execution Command Sheet
Appendix A. Diagram Placeholder Register
Appendix B. Blueprint-to-Execution Mapping
Appendix C. Day-30 / Day-90 Readiness Gates
Day 30 — 8 September 2026
Day 90 — 7 November 2026

1. Executive Summary

Newwaves is not beginning Konn3ct Edge from a blank sheet. It already has two valuable Version 1 assets: a delivered white-labelled 1Gov platform and a new Konn3ct Version 1 currently under active testing. The strategy is therefore an evolutionary transformation, not an unnecessary rebuild. The first obligation is to protect what works, learn from what is live, stabilise what is weak, converge reusable capabilities into a common core, and progressively implement the Konn3ct Edge Blueprint.

The programme has four simultaneous outcomes: build a better product, build a repeatable execution system, build internal capability and culture, and build measurable market adoption. The Newwaves Project Management Module in Odoo 19 Enterprise becomes the execution control system for all four outcomes. By Day 30 it must be operational with the principal integrations. By Day 90, Konn3ct must target 10,000 qualifying Free Users and 300 qualifying Paid Users while demonstrating substantial technical, mobile, QA, commercial, marketing and operational progress.

Core Management Proposition

Konn3ct Edge and 1Gov will be used as the live laboratories through which Newwaves learns the operating discipline it intends to use across future projects: BUILD → USE → LEARN → IMPROVE → STANDARDISE → SCALE.

FIGURE 1.1 PLACEHOLDER — Konn3ct Edge Strategy Architecture

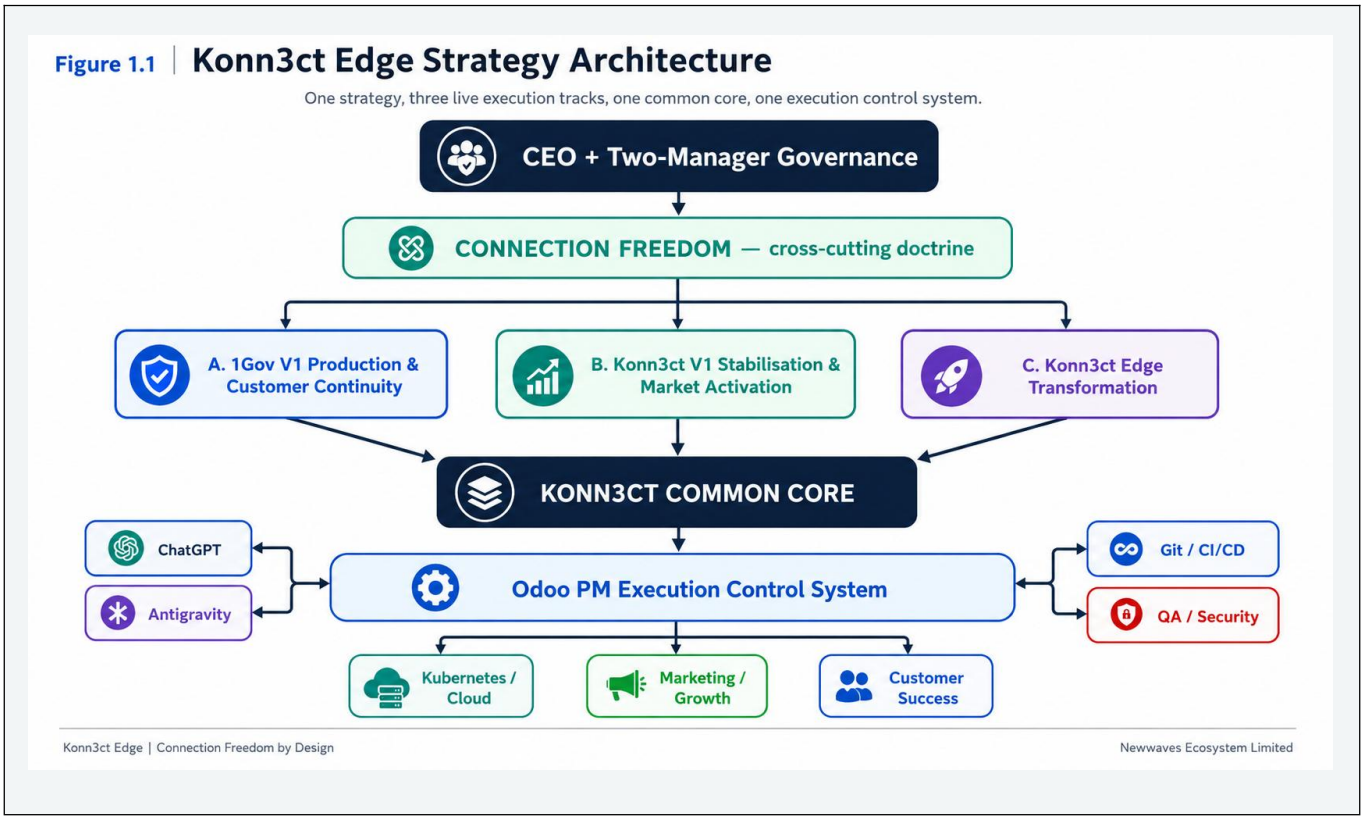


Figure 1.1. Konn3ct Edge Strategy Architecture. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

1.1 Non-Negotiable Outcomes

Horizon	Outcome	Evidence of Success
Day 30 – 8 Sep 2026	PM Execution Control System and primary integrations operational	End-to-end project lifecycle demonstrated; dashboards live; Konn3ct and 1Gov managed inside Odoo; weekly sub-sprints running.

Horizon	Outcome	Evidence of Success
Day 45 – 23 Sep 2026	Market activation gate	Stable-enough core journey, Free/Paid proposition, payment/subscription/entitlement path, usable web/mobile, analytics, CRM and initial Connection Freedom campaigns.
Day 60 – 8 Oct 2026	Growth engine operating	Acquisition, conversion, onboarding, support, CRM, marketing automation and product analytics running; growth run-rate forecast visible.
Day 90 – 7 Nov 2026	Execution + Product + Market gate	10,000 qualifying Free Users; 300 qualifying Paid Users; stable core, meaningful mobile improvement, QA/CI/CD/security gates, Kubernetes foundation, active marketing and customer-success engine.
Year 1 – 9 Aug 2027	Repeatable growth and operating system	52-week marketing cadence, proven channels, improved retention/conversion, stronger common core, sector and partner growth, enterprise scale work materially advanced.
18 Months – 31 Jan 2028	Initial Blueprint implementation	Volumes 1–12 substantially implemented, evidenced and transferred into continuous operations.

2. Current-State Reality and Starting Assets

2.1 1Gov Version 1 — Protected Production and Customer Reference

1Gov is the first white-labelled production/reference implementation that proves Newwaves can deliver a controlled Konn3ct-based platform to an institutional customer. It should be treated as a protected customer track, a source of operational evidence and a controlled recipient of common-core improvements—not as an experimental branch.

- Protect customer continuity and contractual commitments.
- Maintain a dedicated 1Gov release/acceptance ring before production changes.
- Capture defects, support cases, deployment lessons and customer feedback in a 1Gov → Edge Learning Register.
- Classify every issue as 1Gov-specific, common-core, Konn3ct-wide or future Edge requirement.
- Use 1Gov as a government-market reference only within customer-approved confidentiality boundaries.

2.2 New Konn3ct Version 1 — Current Product and Market Baseline

The new Konn3ct Version 1 currently under testing becomes the immediate product stabilisation and market-activation baseline. The strategy should obtain early market evidence from this version while the deeper Edge transformation continues. It is the fastest route to learning whether Connection Freedom, onboarding, pricing, payments, mobile and user acquisition work in practice.

- Complete the active test backlog and stabilise the high-impact user journeys.
- Instrument registration, joining, meeting success, mobile continuity, payment and conversion.
- Use controlled acquisition before full market scale.
- Move reusable fixes into the common core.
- Do not delay learning by waiting for every future Edge capability.

2.3 Konn3ct Edge — Progressive Transformation

Konn3ct Edge is the controlled implementation of Blueprint Volumes 1–12. It should progressively improve architecture, UX, mobile, QA, commercialisation, security, ecosystem and scalability while protecting the two live Version 1 baselines.

FIGURE 2.1 PLACEHOLDER — Three-Track Execution Model

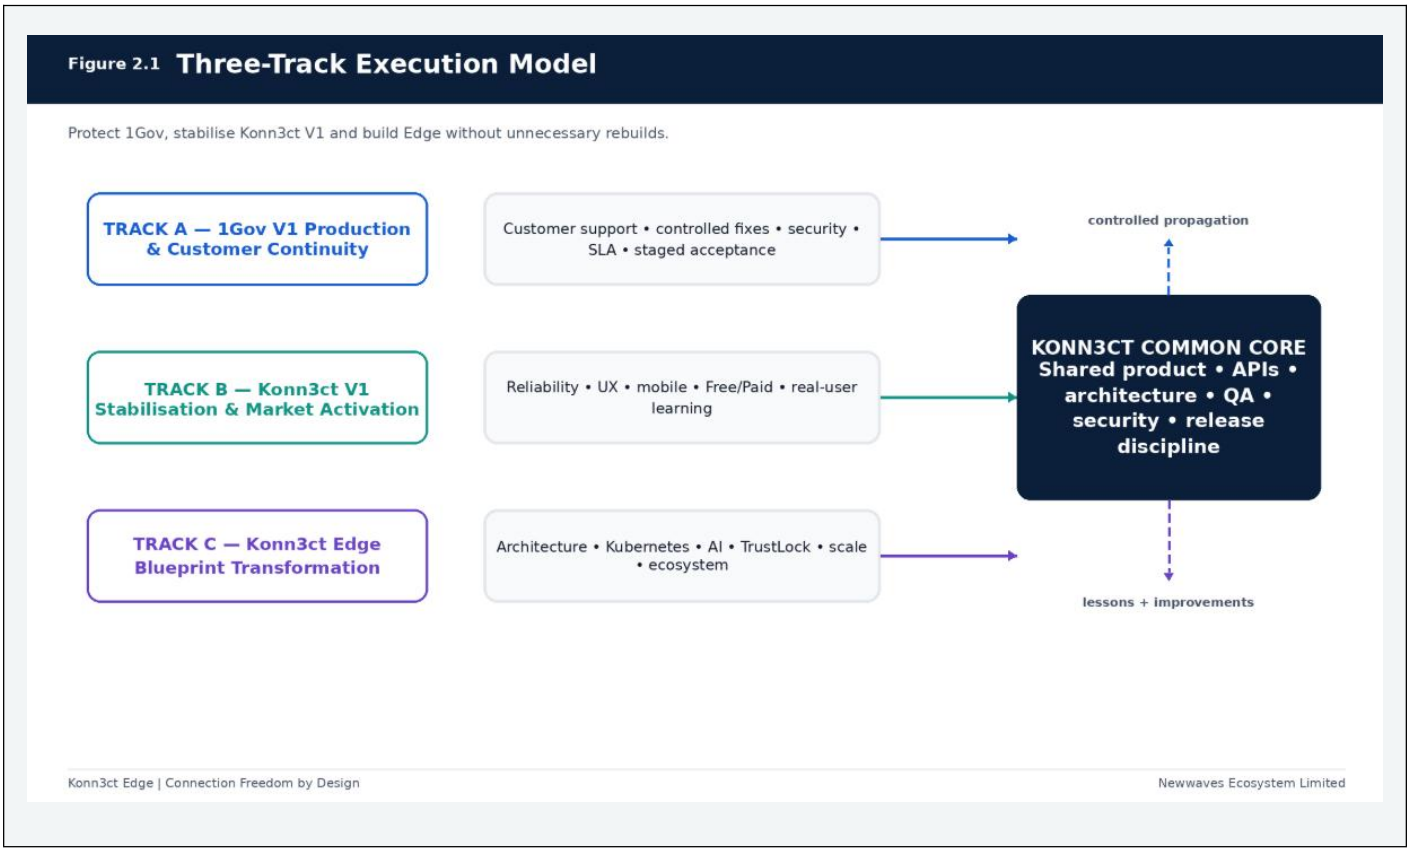


Figure 2.1. Three-Track Execution Model. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

2.4 Retain–Stabilise–Converge Decision Model

Decision	Use When	Required Evidence
Retain	Component works, is supportable and aligns with future direction.	QA evidence, acceptable security/licensing, compatible architecture.
Stabilise	Component is fundamentally useful but unreliable.	Defect pattern and remediation plan.
Improve/Extend	Current component can meet Edge requirements with bounded changes.	Gap analysis and regression plan.
Refactor	Structure creates technical debt but behaviour should be preserved.	Architecture decision record and test baseline.
Converge to Common Core	Capability is duplicated across Konn3ct/1Gov and should be shared.	Tenant compatibility analysis.
Backport/Forward-port	A fix or capability should move safely between supported tracks.	Release-ring testing and tenant impact assessment.
Replace/Rebuild	Current solution cannot meet target requirements economically or safely.	Documented technical, security, licensing or performance justification.
Retire/Defer	Low-value or obsolete capability should stop consuming priority.	Product decision and customer impact check.

3. Connection Freedom by Design

Connection Freedom is the central doctrine governing product, experience, architecture, quality, support and market positioning. The approved Connection Freedom Doctrine and its six freedoms are authoritative. The execution system should reference them through CF-1 to CF-6 identifiers mapped directly to the approved wording.

Primary Product Gate

For every major capability ask: Does this increase or reduce the user's freedom to connect successfully, simply, securely and confidently?

3.1 Experience Principles

Principle	Operational Meaning	Example Measure
Simplicity	Remove unnecessary steps and technical knowledge from joining, hosting and paying.	Time-to-join; funnel completion.
Choice	Offer appropriate device, network, access and commercial choices without arbitrary restriction.	Cross-platform completion rate.
Continuity	Preserve sessions through network, background/foreground and temporary interruption where technically possible.	Reconnect success; mobile recovery.
Accessibility	Design for different abilities, technology familiarity, device capabilities and conditions.	Accessibility test pass rate.
Device Independence	Supported web/mobile clients should provide dependable core journeys.	Compatibility certification coverage.
Network Resilience	Adapt before failing; degrade gracefully where possible.	Weak-network meeting success.
Trust	Security controls should be visible, predictable and proportionate.	TrustLock incidents; user comprehension.
Recoverability	A recoverable fault should not force avoidable abandonment.	Recovery time and success.
Human-Centred AI	AI assists users and operators while material control remains human-governed.	AI exception rate; human approval compliance.

FIGURE 3.1 PLACEHOLDER — Connection Freedom Strategic Model

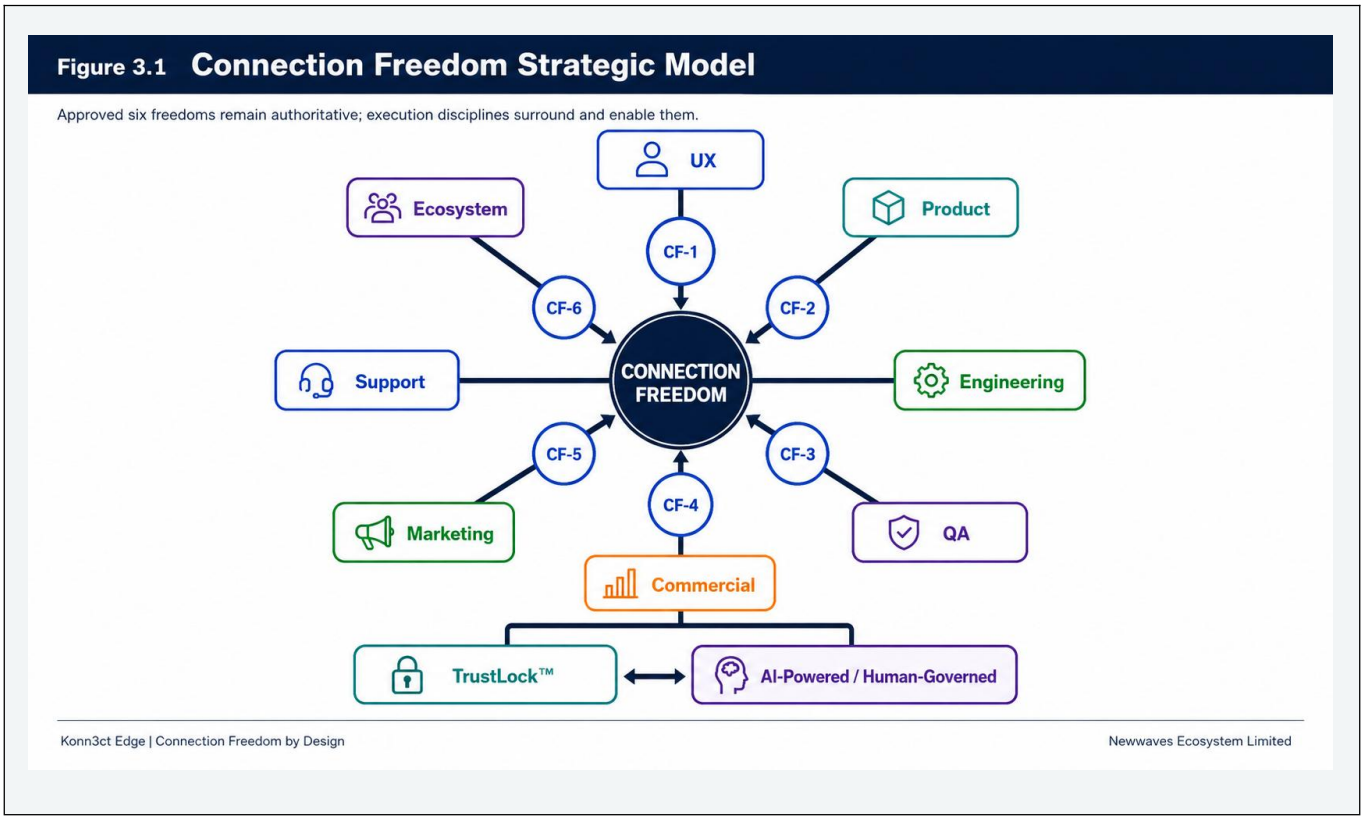


Figure 3.1. Connection Freedom Strategic Model. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

3.2 Connection Freedom Index (CFI)

The CFI should be an operational composite index, not a marketing vanity score. Its final weights should be approved after 30 days of baseline data. Until then, use a provisional weighted model and review it monthly.

Evidence Category	Provisional Weight	Data Source
Successful join / time-to-join	15%	Product analytics, QA
Audio/video success	15%	WebRTC telemetry, QA
Reconnection and recovery	15%	Client/service telemetry
Mobile continuity	10%	Mobile analytics/crash monitoring
Network resilience	10%	QA scenario results and telemetry
Compatibility/accessibility	10%	Certification matrix
Recording/replay/payment completion	10%	Platform + commercial analytics
Trust/security experience	5%	TrustLock/security events
Support recovery	5%	Odoo Helpdesk
User satisfaction	5%	Survey/NPS/CSAT

Release policy: no major release should materially reduce the CFI without an explicitly documented and approved trade-off. The CFI should appear in the CEO, Growth, Technology and release dashboards.

4. Organisation, Governance and Decision Rights

4.1 CEO and Two-Manager Operating Model

Role	Primary Accountability	Escalation / Approval
CEO	Vision, strategic direction, major investment, major release, material risk acceptance, Steering Committee.	Final escalation; major architecture/commercial decisions.
Growth & Ecosystem Manager	Conceptualisation, product requirements, UX, Connection Freedom, marketing, Free/Paid growth, commercialisation, onboarding, customer success, partnerships.	Accountable for user, market and commercial outcomes.
Technology & Business Operations Manager	Architecture, engineering, mobile, WebRTC, Odoo, PM module, AI implementation, DevOps, Kubernetes, QA, cybersecurity, licensing, reliability and production operations.	Accountable for technical, quality, security and operational outcomes.

FIGURE 4.1 PLACEHOLDER — CEO / Two-Manager Governance Diagram

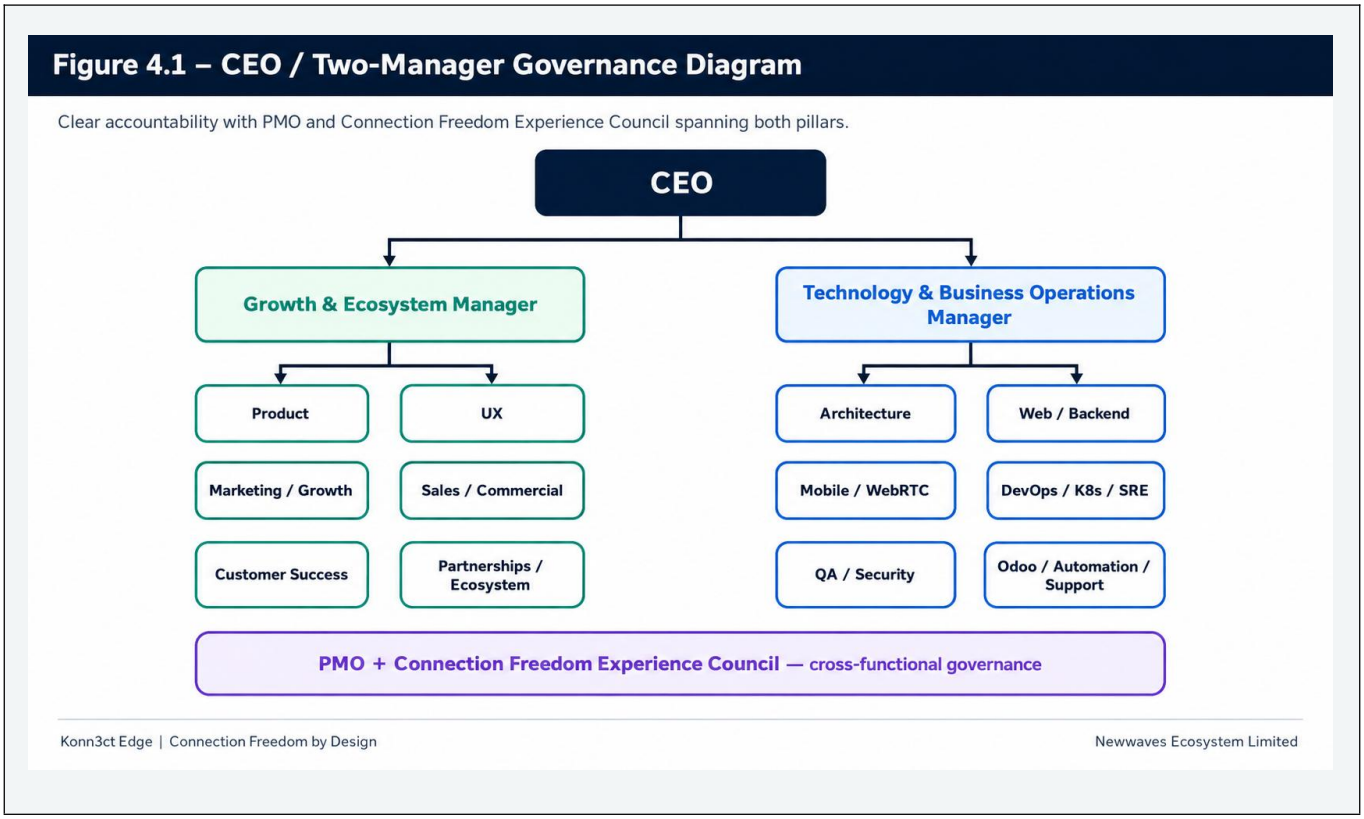


Figure 4.1. CEO / Two-Manager Governance Diagram. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

4.2 Key Governance Bodies

Body	Chair	Cadence	Mandate
Konn3ct Edge Steering Committee	CEO	Monthly	Strategy, funding, cross-functional decisions, major risks.
Connection Freedom Experience Council	Growth & Ecosystem Manager	Weekly/biweekly	UX journeys, friction, accessibility, CFI, customer experience.

Body	Chair	Cadence	Mandate
Architecture Review Board	Technology & Business Operations Manager	As required + monthly	ADRs, common-core boundaries, integrations, platform architecture.
Release & Quality Board	QA Lead	Per release	QA evidence, release blockers, UAT, go/no-go recommendation.
Security & Privacy Gate	Security Lead	Per major change/release	Threats, controls, vulnerabilities, privacy and risk acceptance.
Growth Command Review	Growth & Ecosystem Manager	Weekly	Free/Paid run rate, funnel performance, channel allocation, market actions.
PMO Portfolio Review	PMO/Project Lead	Weekly	Sprint score, dependencies, milestones, risks, workload, carry-over.

4.3 QA Independence

QA may report operationally through Technology & Business Operations, but the QA Lead must be empowered to reject a release, classify release-blocking defects, require retesting, request security review and escalate unresolved quality risks directly to the CEO. Development may not finally certify its own work.

5. Newwaves Project Management Execution Control System

The Odoo 19 Enterprise Project Management Module is the central operational system of record for execution. It is not an administrative reporting tool. It is the mechanism through which work is initiated, owned, evidenced, tested, approved, deployed, measured and learned from.

FIGURE 5.1 PLACEHOLDER — Execution Control Architecture

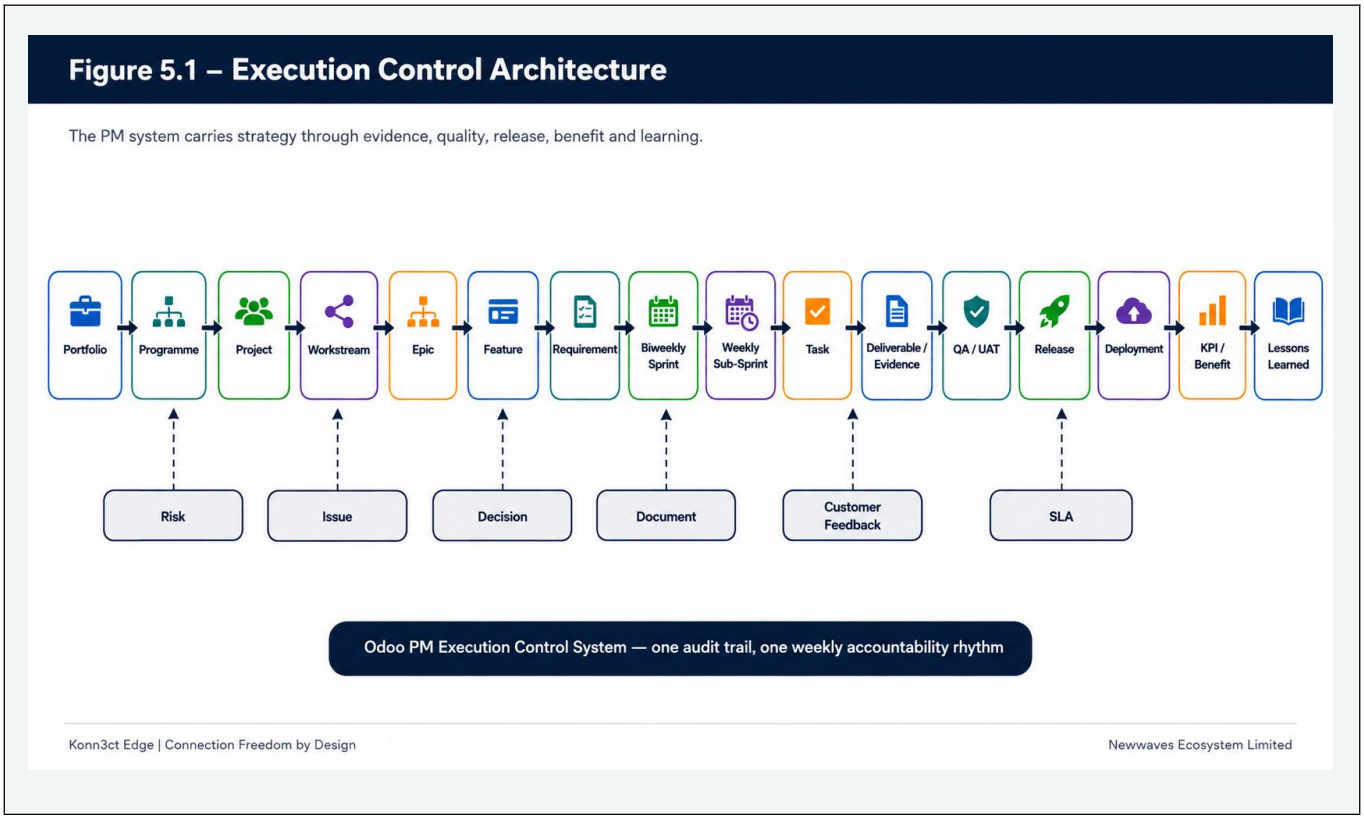


Figure 5.1. Execution Control Architecture. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

5.1 Core Odoo Data Model

Object	Purpose	Minimum Fields
Portfolio	Executive grouping of programmes.	Owner, objective, budget, status, benefits, strategic linkage.
Programme	Coordinates related projects.	Sponsor, manager, dates, dependencies, KPIs, milestones.
Project	Execution unit.	Customer/tenant, owner, Blueprint linkage, environment, budget, status.
Workstream	Functional slice.	Lead, deliverables, dependencies, KPI.
Requirement	Approved need.	ID, user problem, CF reference, Blueprint volume, acceptance criteria, owner, priority.
Sprint	Two-week planning container.	Goal, start/end, capacity, parent workstream, release.
Weekly Sub-Sprint	Management execution unit.	Weekly outcomes, owners, score, evidence, risks, carry-over.
Task/Subtask	Assignable work.	Owner, due date, estimate, dependency, evidence, status.
Defect	Quality issue.	Severity, environment, steps, evidence, owner, retest, release blocker.
Test Case	Validation evidence.	Scenario, device/browser/OS, expected, actual, status, evidence.
Release	Approved package.	Scope, build, tests, security, UAT, approvers, deployment plan, rollback.
Risk/Issue/Decision	Governance records.	Impact, probability/status, owner, due date, decision authority.
Customer Feedback	Voice of customer.	Customer, journey, classification, priority, linked requirement/defect.
Benefit/KPI	Outcome tracking.	Baseline, target, actual, source, owner, period.

5.2 End-to-End Lifecycle

Stage	Mandatory Exit Evidence
Strategic Intake	Approved record/evidence captured in Odoo before transition.
Concept	Approved record/evidence captured in Odoo before transition.
Connection Freedom Assessment	Approved record/evidence captured in Odoo before transition.
Value/KPI Assessment	Approved record/evidence captured in Odoo before transition.
Prioritisation	Approved record/evidence captured in Odoo before transition.
Steering Approval	Approved record/evidence captured in Odoo before transition.
Business Requirement	Approved record/evidence captured in Odoo before transition.
Acceptance Criteria	Approved record/evidence captured in Odoo before transition.
UX/User Journey	Approved record/evidence captured in Odoo before transition.
Technical Design	Approved record/evidence captured in Odoo before transition.
Architecture Review	Approved record/evidence captured in Odoo before transition.
Security Review	Approved record/evidence captured in Odoo before transition.
Sprint Ready	Approved record/evidence captured in Odoo before transition.
Development	Approved record/evidence captured in Odoo before transition.
Developer QA	Approved record/evidence captured in Odoo before transition.
Code Review	Approved record/evidence captured in Odoo before transition.

Stage	Mandatory Exit Evidence
Functional QA	Approved record/evidence captured in Odoo before transition.
Integration QA	Approved record/evidence captured in Odoo before transition.
Regression QA	Approved record/evidence captured in Odoo before transition.
Performance QA	Approved record/evidence captured in Odoo before transition.
Security QA	Approved record/evidence captured in Odoo before transition.
UAT	Approved record/evidence captured in Odoo before transition.
Product Acceptance	Approved record/evidence captured in Odoo before transition.
Release Candidate	Approved record/evidence captured in Odoo before transition.
Go/No-Go	Approved record/evidence captured in Odoo before transition.
Deployment	Approved record/evidence captured in Odoo before transition.
Production Verification	Approved record/evidence captured in Odoo before transition.
Hypercare	Approved record/evidence captured in Odoo before transition.
Customer Feedback	Approved record/evidence captured in Odoo before transition.
Benefits/KPI Tracking	Approved record/evidence captured in Odoo before transition.
Continuous Improvement	Approved record/evidence captured in Odoo before transition.
Closure	Approved record/evidence captured in Odoo before transition.

5.3 Weekly Sub-Sprint Operating Unit

Engineering may use two-week sprints, but management accountability operates weekly. Every biweekly sprint is split into two weekly sub-sprints with measurable outcomes and a Friday evidence review.

Field	Required Content
Identity	Sprint ID, week number, dates, parent sprint, project/workstream.
Strategic Linkage	Blueprint Volume, CF reference, business objective.
Outcomes	User, technical, commercial and marketing outcomes as applicable.
Ownership	Responsible manager, workstream lead, individual owners.
Delivery	Deliverables, dependencies, blockers, risks, planned effort.
Acceptance	Acceptance criteria, test evidence, required approvals.
Performance	Planned vs actual completion, variance, RAG, KPI impact.
Learning	Capability transfer, lesson learned, carry-over, next action.

5.4 Weekly Sprint Score

Component	Weight
Deliverables achieved	30%
Acceptance criteria passed	20%
Quality/test results	15%
Schedule adherence	10%
Connection Freedom impact	10%
Risk/blocker management	5%
Documentation/evidence	5%

Component	Weight
Capability transfer	5%

Recommended thresholds: Green ≥ 85; Amber 70–84; Red < 70. A Green score cannot override a critical security, quality or customer-impact blocker.

5.5 Weekly Management Rhythm

Day	Forum	Primary Question	Odoo Output
Monday	Sub-Sprint Commitment	What measurable outcomes will be delivered this week?	Committed outcomes, capacity, dependencies, owners.
Tuesday–Thursday	Execution	What is moving, blocked or failing?	Live task/build/test/risk status.
Friday	Evidence & Outcome Review	What outcome did we actually produce and prove?	Sprint score, evidence, KPI effect, lessons, carry-over.
Friday	Growth Command Review	Are Free/Paid trajectories improving or slipping?	Run-rate forecast and next-week channel/product actions.

Culture Rule
Evidence replaces narration. “Done” means the approved acceptance criteria are met and objective evidence is attached.

6. First 30 Days — PM and Integration Go-Live

The PM system must be built while being used. Konn3ct and 1Gov should be entered into the emerging system during Week 1 so missing fields, workflow friction, permission issues and reporting gaps are discovered before Day 30.

Week	Dates	Theme	Must Deliver
Week 1	10–16 Aug	PM Foundation & Mobilisation	Programme charter; portfolio/programme/project hierarchy; RACI; lifecycle; Odoo base; Konn3ct and 1Gov projects; users/security groups; requirement/risk/issue/decision registers; first dashboards.
Week 2	17–23 Aug	Workflows & Traceability	Requirements, acceptance criteria, sprints, weekly sub-sprints, dependencies, QA, defects, releases, change/decision/document flows, traceability IDs, alerts; begin Git/ChatGPT/Antigravity integration.
Week 3	24–30 Aug	Integrations & Automation	Git, CI/CD, ChatGPT/OpenAI, Antigravity, QA/testing, Kubernetes/infra monitoring, Konn3ct/1Gov events, Helpdesk, CRM, Documents, Knowledge; automated build/test/defect/status events.
Week 4	31 Aug–6 Sep	Dashboards, Portal & Control	CEO/manager/PM/QA dashboards, customer portal, approvals, feedback/UAT, weekly score, capability maturity, full PM UAT.

Week	Dates	Theme	Must Deliver
Days 29–30	7–8 Sep	Hardening & Go-Live	Security/permissions, portal isolation, integration tests, backup/audit verification, staff training, management acceptance, support handover, production go-live.

FIGURE 6.1 PLACEHOLDER — 30-Day PM & Integration Roadmap

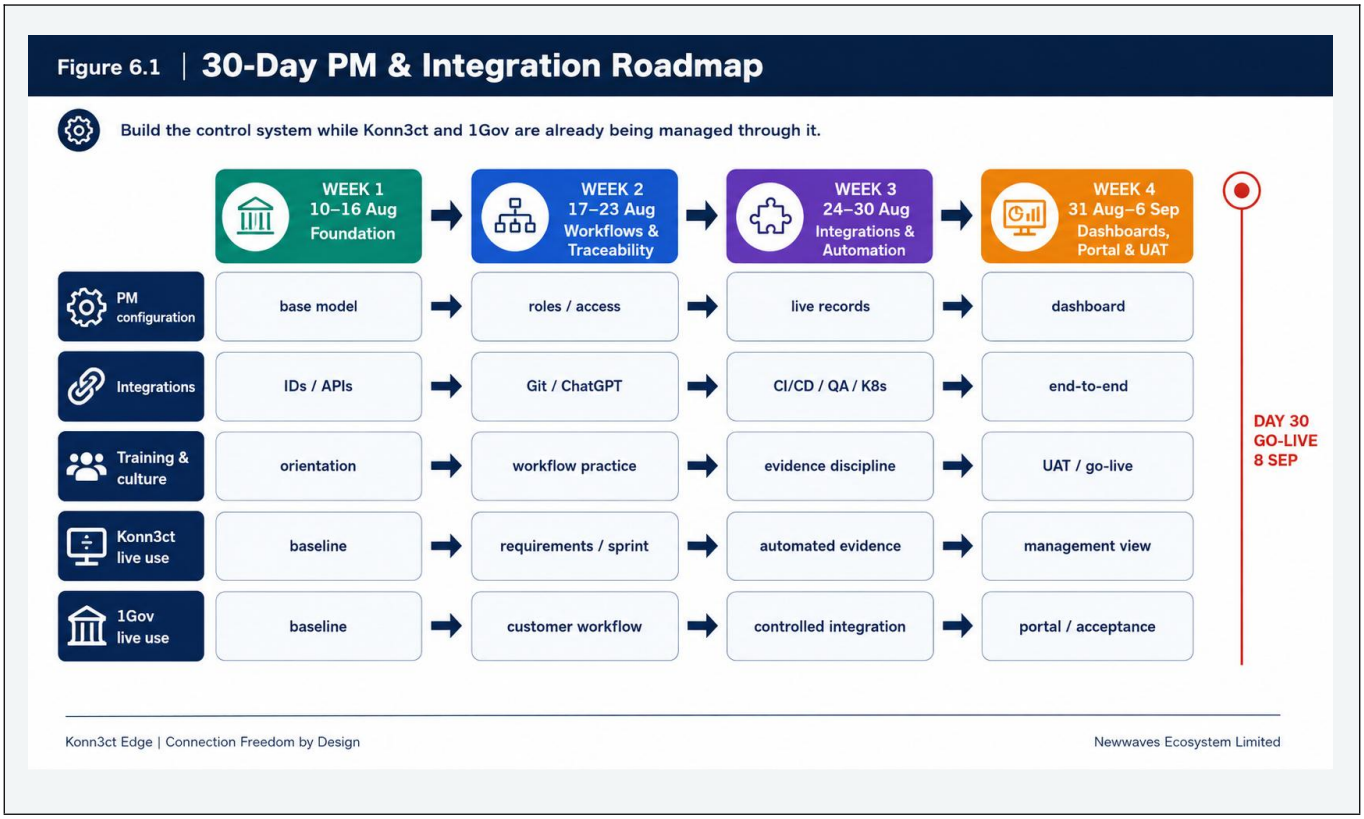


Figure 6.1. 30-Day PM & Integration Roadmap. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

6.1 Day-30 Acceptance Test

1. Create portfolio, programme, project and workstream.
2. Create a Blueprint-linked requirement and approve it.
3. Create a biweekly sprint and two weekly sub-sprints.
4. Assign tasks, dependencies, due dates and evidence requirements.
5. Receive or attach engineering/Git/CI information.
6. Record QA, create defect and retest.
7. Conduct UAT and product acceptance.
8. Create release, approve it and record deployment/rollback.
9. Capture customer feedback and SLA/support activity.
10. Display CEO, manager and PMO dashboards.
11. Expose only approved customer data through the portal.
12. Generate weekly sprint performance and preserve audit history.

7. Tool Architecture, Systems of Record and Integrations

7.1 Systems of Record

Information	Authoritative System	Supporting Systems
Approved strategy / Blueprint / Doctrine	Approved document repository + Odoo document reference	ChatGPT for analysis; Knowledge for summaries.
Requirements, tasks, sprints, risks, decisions	Odoo PM Execution Control	ChatGPT/Antigravity may draft but not supersede approved Odoo record.
Source code	Git repository	Antigravity and CI/CD operate through controlled repository access.
Architecture decisions	Odoo/Docs ADR register	Git-linked technical documents.
Tests and release evidence	Odoo QA records + CI artefacts	Testing systems, Git/CI logs.
Customers, leads, subscriptions, Helpdesk	Odoo CRM/Sales/Subscriptions/Helpdesk	Konn3ct operational systems synchronise identifiers/status.
Infrastructure configuration	Infrastructure-as-Code repository	Kubernetes/cloud platform is runtime state.
Monitoring/telemetry	Observability platform	Summaries and incidents synchronised to Odoo.
Financial transactions	Odoo Accounting / approved payment records	Payment gateway event data.
Marketing campaign activity	Odoo Marketing + analytics platform	Website/social/email platforms.
Executive decisions	Odoo Decision Register	Meeting notes/supporting analysis may live elsewhere but must be summarised into Odoo.

7.2 Integration Principles

- Use secure APIs/webhooks/MCP where actually supported; do not design around imagined interfaces.
- Prefer event-driven integration for build/test/deployment/customer events and scheduled reconciliation for lower-urgency data.
- Use correlation IDs so Odoo requirement IDs appear in branches, commits, pull requests, test results and releases.
- Use service accounts, least privilege, signed payloads and idempotent event handling.
- Design a manual fallback for critical workflows, but treat copy/paste as temporary rather than the target state.

FIGURE 7.1 PLACEHOLDER — People–Process–Tools Integration Architecture

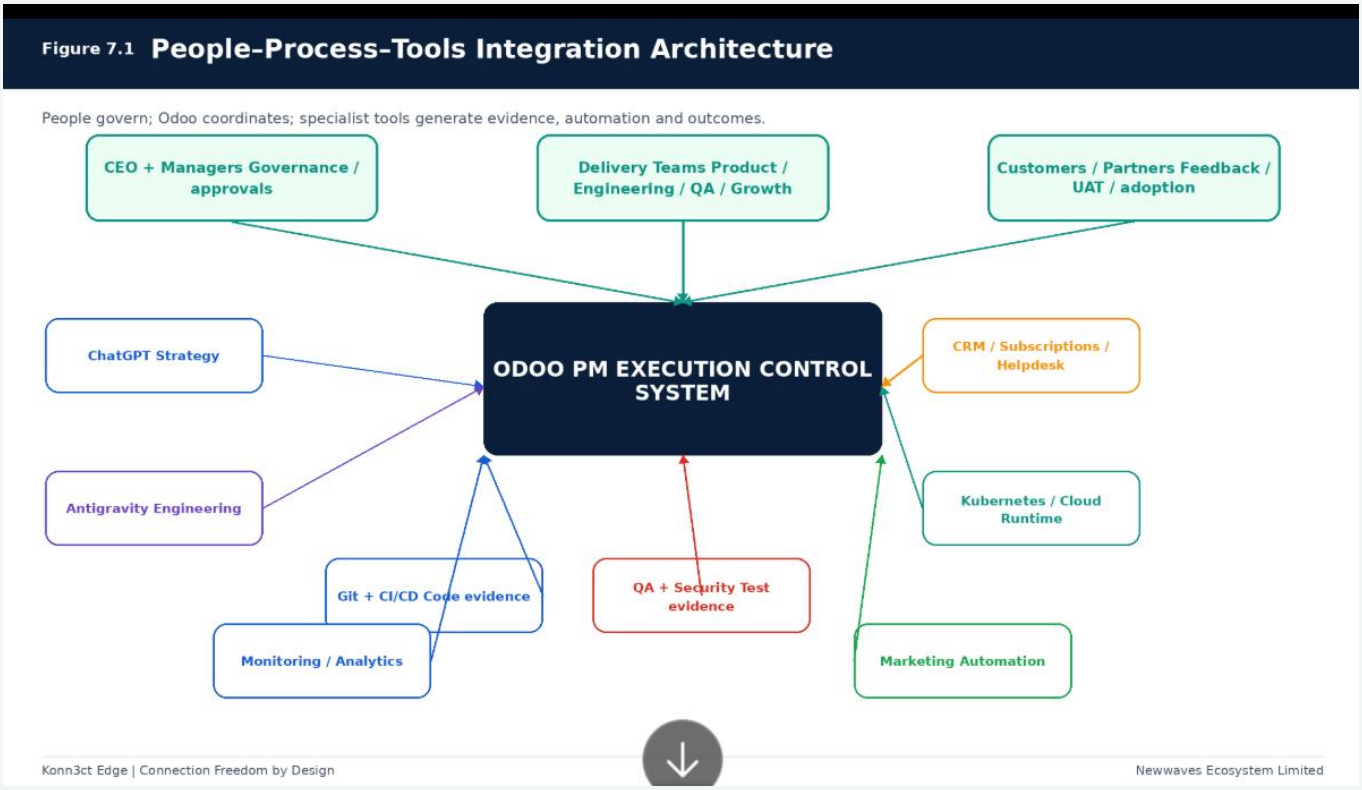


Figure 7.1. People–Process–Tools Integration Architecture. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

8. ChatGPT as Strategy Partner

ChatGPT should operate as an ongoing strategy, synthesis, review and decision-support partner. It should not become an ungoverned system of record or replace accountable managers. The approved strategy document and approved Odoo decisions form its principal governance context.

8.1 Strategy Partner Operating Instructions

- Maintain alignment to Blueprint Volumes 1–12 and the approved Connection Freedom Doctrine.
- Identify conflicts between new requests and approved strategy rather than silently changing direction.
- Review weekly sprint packs, growth trajectory, risks, architecture, customer feedback and marketing evidence.
- Recommend priorities and trade-offs, but leave accountable approval to humans.
- Use newer formally approved Odoo decisions as authoritative where they supersede the strategy; recommend a formal strategy update where material.
- Treat 1Gov continuity, Konn3ct V1 reuse and common-core integrity as standing constraints.
- Challenge activity that does not contribute to user outcomes, quality, adoption, revenue, risk reduction or internal capability.

8.2 Recommended AI Workspaces

Workspace	Primary Use	Human Owner
CEO Executive Support	Weekly executive review, decisions, strategic options.	CEO
Blueprint Governance	Requirement alignment and change impact.	CEO/PMO
Product & UX	User journeys, Connection Freedom, prioritisation.	Growth & Ecosystem
Technology Architecture	ADRs, integration, scalability and technical reviews.	Technology & Business Operations

Workspace	Primary Use	Human Owner
Mobile	Mobile quality, release planning, device/network scenarios.	Mobile Lead
WebRTC/Media	Media reliability, large-room architecture, performance.	Media Lead
QA & Release	Test strategy, diagnostic analysis, release evidence.	QA Lead
Security & TrustLock	Threat/control analysis, release risk.	Security Lead
Growth & Marketing	Campaign planning, weekly review, conversion analysis.	Growth & Ecosystem
Commercial	Pricing, packaging, entitlement and revenue analysis.	Growth & Ecosystem/Finance
Customer Success	Onboarding, support patterns, churn/health analysis.	Customer Success Lead
PMO	Sprint review, risk/issue/decision analysis.	PMO

FIGURE 8.1 PLACEHOLDER — ChatGPT–Odoo–Antigravity Orchestration

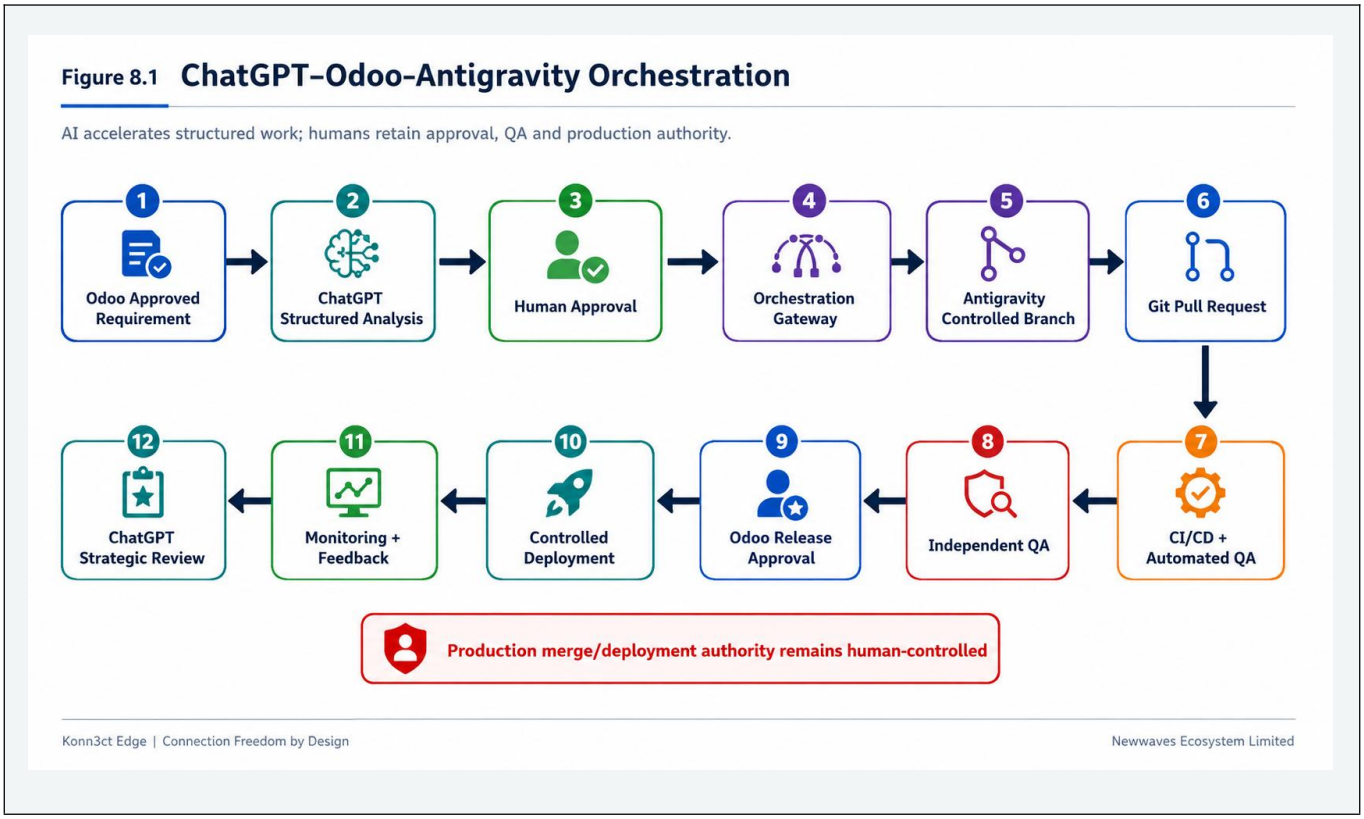


Figure 8.1. ChatGPT–Odoo–Antigravity Orchestration. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

9. Antigravity and Controlled AI-Assisted Engineering

Antigravity should be treated as a controlled engineering agent rather than an autonomous production operator. It receives approved work packages, works inside restricted repositories/branches, produces tests and evidence, and submits changes through standard review and CI/CD gates.

9.1 Mandatory Work-Order Fields

- Project and requirement ID; Blueprint Volume and CF reference.
- Business objective and user problem.
- Current behaviour and required behaviour.
- Affected repositories/files and known dependencies.
- Architecture constraints and common-core/tenant boundaries.

- Acceptance criteria and UX acceptance criteria.
- Security/privacy/licensing requirements.
- Regression requirements: do not damage existing working functionality.
- Testing, documentation, migration and rollback requirements.
- Definition of Done and required evidence.

Mandatory Engineering Rule

Do not break, remove or materially alter existing functioning capabilities outside the approved change scope. Every significant fix should create a permanent regression test where practical.

9.2 AI Autonomy Levels

Level	Permitted	Not Permitted
0 Advisory	Analyse and recommend.	Create/change operational records.
1 Drafting	Draft requirements, plans, tests, documentation.	Approve drafts or change production.
2 Controlled Execution	Create restricted branch, modify code, run tests, prepare PR.	Merge protected branch or deploy production.
3 Restricted Non-Production	Deploy to approved dev/QA, reset test environment, run approved runbook.	Unrestricted secrets or production data changes.
4 Production-Restricted	Assist analysis and prepare recommended actions.	Approve own work, bypass QA/security, accept risk, deploy directly, change pricing/financial controls.

10. Common Core, White-Label Governance and Release Management

The long-term objective is a controlled Konn3ct common core with configuration and extension points for Konn3ct, 1Gov and future white labels. Permanent forks should be avoided because they multiply QA cost, security risk and release complexity.

10.1 Common-Core Rules

- Shared meeting/media, identity, security, recording, payment, analytics and integration primitives belong in the common core unless a documented reason exists otherwise.
- Branding, domains, tenant policies, approved local integrations and selected configuration should remain tenant-level wherever possible.
- Customer-specific code requires architecture approval, compatibility tests and a merge-back/deprecation plan.
- A fix discovered in 1Gov or Konn3ct V1 must be assessed for common-core relevance before a tenant-only patch is accepted.

10.2 Release Rings

Ring	Environment / Audience	Purpose
0	Developer	Fast feedback and unit/integration validation.
1	Internal QA	Independent functional/regression/security quality checks.
2	Konn3ct Controlled Pilot	Real-user pilot and Connection Freedom validation.
3	Konn3ct Production	General Konn3ct release.
4	1Gov Staging / Acceptance	Customer-specific regression and approval.
5	1Gov Production	Controlled customer deployment.

FIGURE 10.1 PLACEHOLDER — Common-Core Convergence and Release Rings

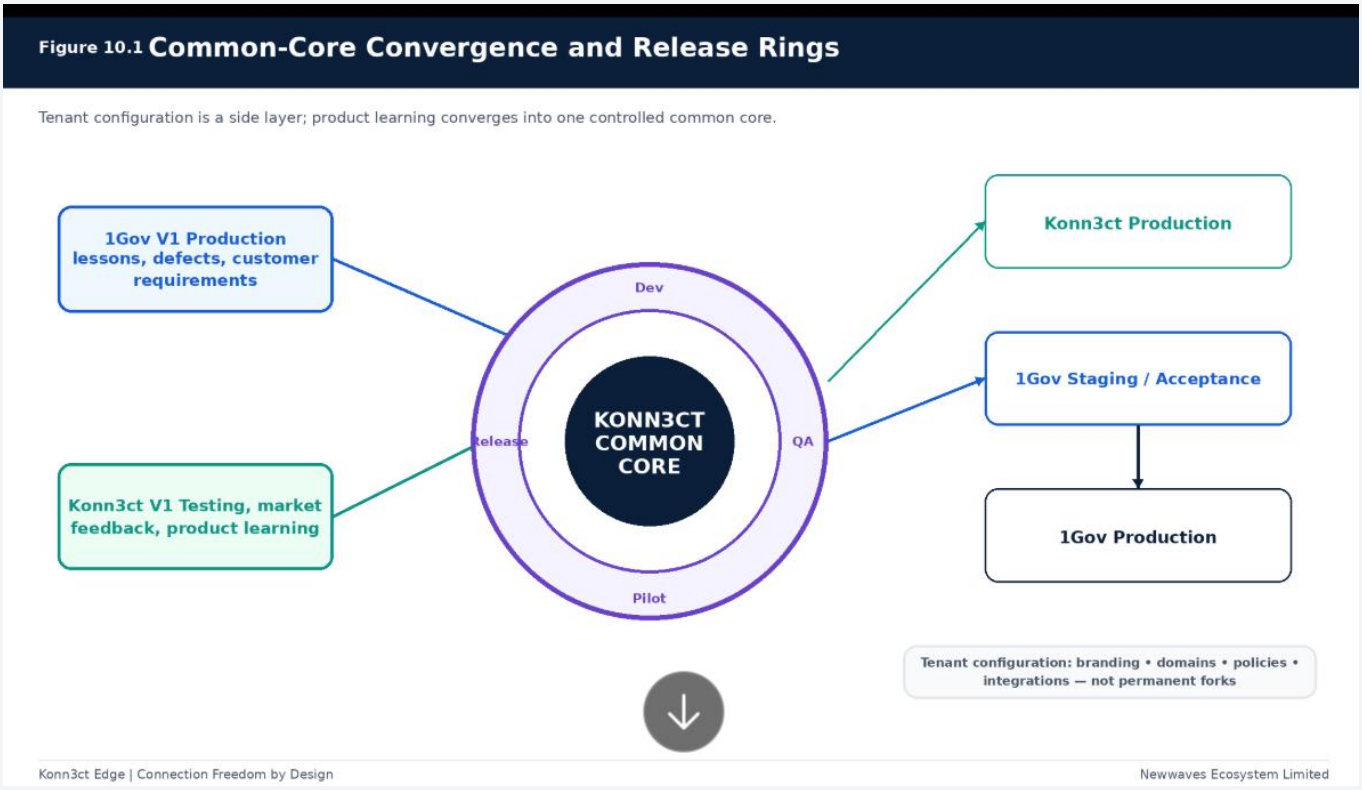


Figure 10.1. Common-Core Convergence and Release Rings. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

11. Blueprint-to-Release Traceability

Every material item must carry a stable identifier so the CEO can trace strategy to implementation and business outcome. A recommended pattern is KE-[Volume]-[Domain]-[Object]-[Sequence].

Object	Example
Requirement	KE-V06-MEDIA-REQ-001
Feature	KE-V04-MOB-FEA-014
Task	KE-V04-MOB-TSK-063
Sprint	KE-SPR-2026-04
Weekly Sub-Sprint	KE-WSS-2026-W08
Test	KE-V07-MOB-TST-112
Defect	KE-V07-MOB-DEF-049
Security Control	KE-V10-SEC-CTL-031
Release	KE-REL-R0-2026-10
Deployment	KE-DEP-1GOV-2026-10-31
Marketing Campaign	KE-V02-MKT-CMP-021
Commercial Outcome	KE-V08-COM-KPI-007

FIGURE 11.1 PLACEHOLDER — Blueprint → Outcome Traceability Chain

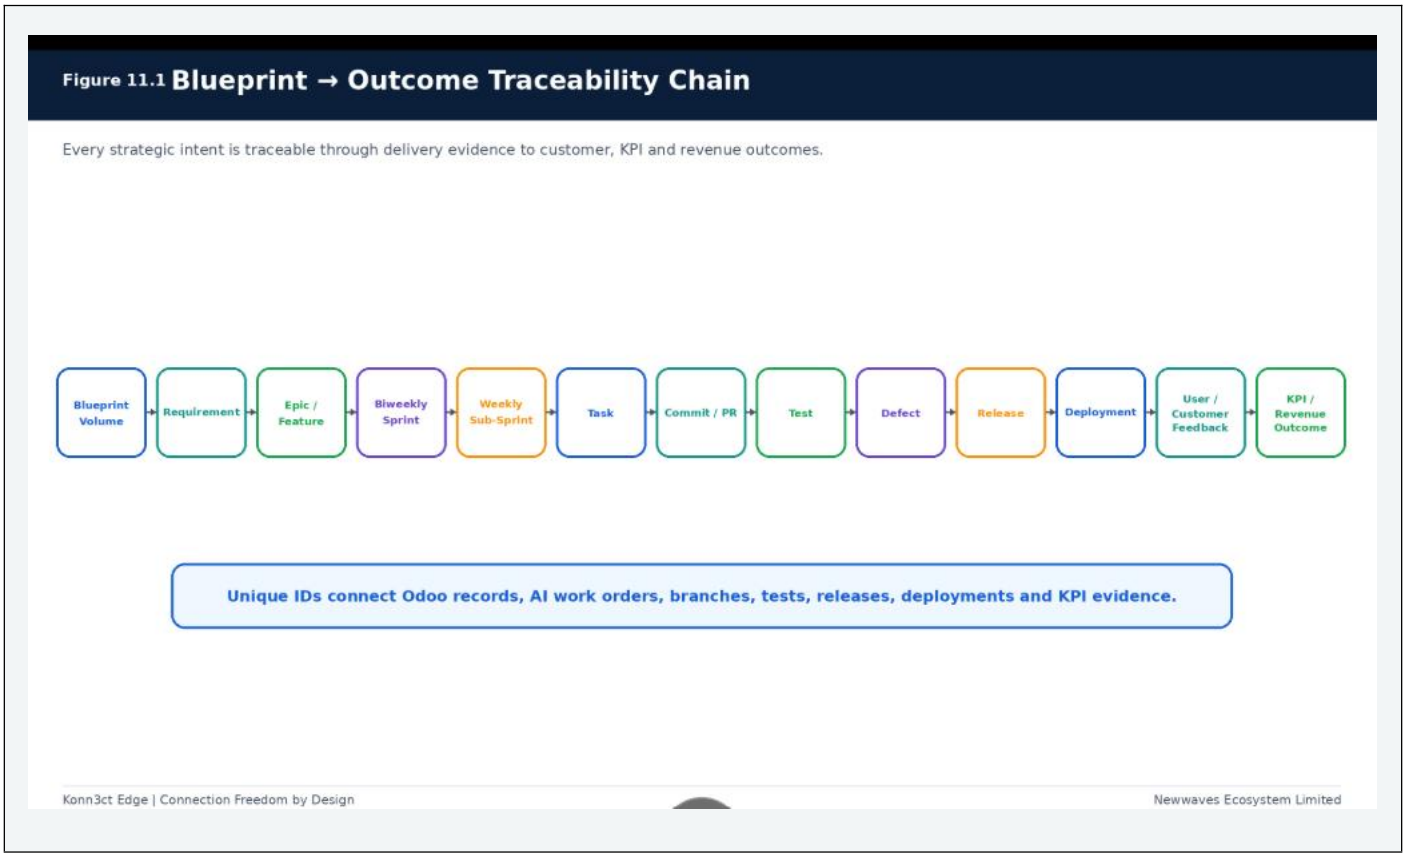


Figure 11.1. Blueprint → Outcome Traceability Chain. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

12. First 90 Days — 13 Weekly Sub-Sprints

The first 90 days are deliberately integrated: PM maturity, product stabilisation, technical architecture, commercial enablement and marketing growth proceed in parallel. The goal is not "build for 90 days, then market." The operating model is BUILD + TEST + LAUNCH + ACQUIRE + LEARN + IMPROVE + CONVERT.

Wk	Dates	Theme	Product/PM/Technology	Weekly Outcome	Marketing/Growth
1	10–16 Aug	Mobilise & Establish Control	PM foundation; current-state baselines; 1Gov/Konn3ct projects; user/growth baseline.	Current assets visible; first Odoo records and dashboards.	Brand/channel/website audit; audience baseline; Connection Freedom message prep.
2	17–23 Aug	Requirements, Workflows & Entry Experience	PM lifecycle/traceability; registration, auth, joining, invitations; Free/Paid definition.	Entry funnel measured and requirements approved.	Segmentation, personas, funnel/landing-page design.
3	24–30 Aug	Toolchain Integration + Core Reliability	Git/ChatGPT/Antigravity/CI integration; audio/video/reconnect; pricing/payment architecture.	Core reliability defects reduced; engineering evidence flowing.	Messaging house, content calendar, CRM capture, early assets.
4	31 Aug–6 Sep	Dashboards, Portal & Market Engine	PM dashboards/portal; onboarding analytics; payment testing.	Management control and growth instrumentation ready.	Landing pages, campaign tracking, email/social templates, referral design.
5	7–13 Sep	PM Go-Live + Controlled Acquisition	PM production; stabilisation release; support/onboarding.	Real project execution in PM; controlled user acquisition begins.	Early campaigns, direct outreach, invite growth; daily funnel measurement.
6	14–20 Sep	Media Reliability + Paid Conversion	Audio/video/reconnect/mobile; Paid plan/payment/entitlement/subscription.	Paid conversion technically possible; quality metrics visible.	Paid proposition, upgrade messages, lead nurturing, testimonial capture.

Wk	Dates	Theme	Product/PM/Technology	Weekly Outcome	Marketing/Growth
7	21–27 Sep	Day-45 Market Activation	Core market-ready proposition; defects from live users fixed rapidly.	Stable enough journey for broader acquisition.	Connection Freedom campaign, demos/webinars, partner/referral, enterprise/government outreach.
8	28 Sep–4 Oct	Mobile-Led Growth	Mobile join/reconnect/background/notifications/permissions; cross-device quality.	Mobile contributes materially to acquisition and activation.	QR/app/mobile acquisition and community campaigns.
9	5–11 Oct	Day-60 Growth Engine	Funnel instrumentation, payment/meeting abandonment analysis, top barrier removal.	Acquisition and conversion engines operating.	Channel optimisation, retargeting, referral reinforcement.
10	12–18 Oct	Conversion Optimisation	Prioritise signup/join/payment/repeat-use blockers.	Conversion and activation improve week-over-week.	Nurture, proof/testimonials, high-performing channel scale.
11	19–25 Oct	Growth + Platform Scale	Kubernetes foundation, room allocator, capacity/monitoring; growth blockers.	Infrastructure ready for higher demand.	Partnerships, events, enterprise/government/community scale.
12	26 Oct–1 Nov	Target Closing Sprint	Reliability, payment, onboarding, referral and conversion blockers only.	Maximum probability of hitting Day-90 KPI.	Acquisition/conversion/reactivation sprint; budget reallocation to best channels.
13	2–7 Nov	90-Day Outcome Gate	Integrated QA, security, load, mobile, commercial and Blueprint review.	Formal readiness report; next-quarter backlog; lessons.	Final 90-day acquisition push and channel review; Year-1 plan reset based on evidence.

FIGURE 12.1 PLACEHOLDER — 13-Week Integrated Execution Roadmap

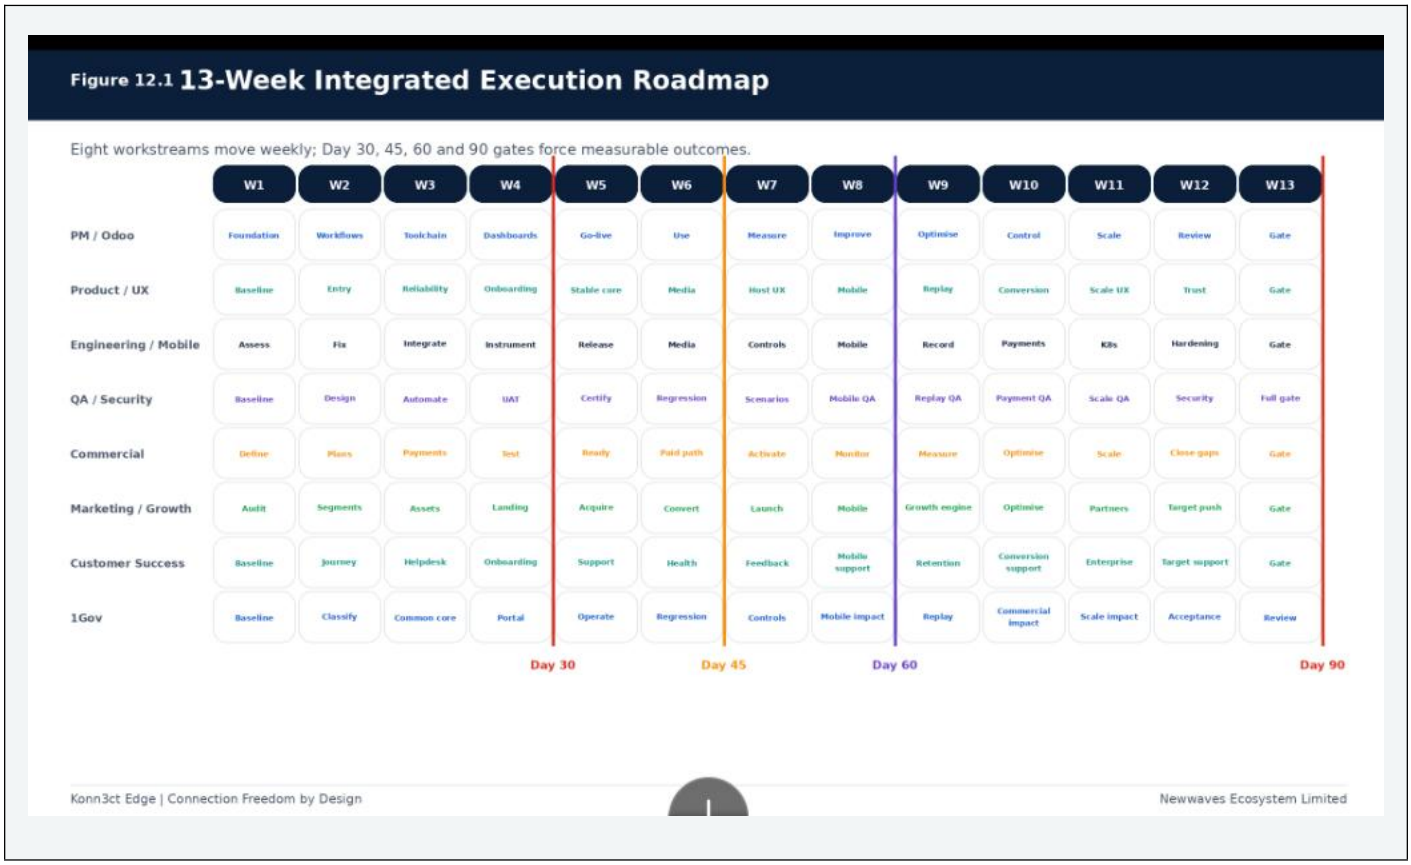


Figure 12.1. 13-Week Integrated Execution Roadmap. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

13. Day-90 Growth Objective — 10,000 Free / 300 Paid

The Day-90 goals are business outcomes and must shape delivery sequencing. Sufficient product, commercial, analytics, onboarding, support and marketing modules must be completed early enough to acquire and convert users during the 90 days.

13.1 Qualifying User Definitions

Metric	Recommended Definition
Registered Free User	Unique legitimate account with valid registration and no duplicate/test/bot status.
Activated Free User	Registered user who completes a meaningful action such as attending/creating a meeting or other approved activation event.
Active Free User	Activated user with qualifying activity in the defined rolling period.
Paid User	Unique customer/account with successful payment or approved contracted entitlement, active paid product entitlement and auditable commercial record.

The CEO should approve which Free User definition is the official 10,000 target. The dashboard should always show Registered, Activated and Active counts side by side to prevent vanity reporting.

13.2 Run-Rate Management

If the programme started from zero qualifying users, a simple 13-week average would require roughly 770 new Free Users and 23 new Paid Users per week. In practice, use the actual baseline and a ramped target curve because the first weeks are setup-heavy and acquisition should accelerate after the Day-45 market gate.

Management Measure	Formula / Rule
Net-new Free required	10,000 – qualifying Free baseline at Day 1
Net-new Paid required	300 – qualifying Paid baseline at Day 1
Required weekly run rate	Remaining target ÷ remaining weeks
Projected Day-90 outcome	Current cumulative + rolling average × remaining weeks
Growth alert	Amber if forecast < 95% of target; Red if forecast < 85% unless an approved catch-up plan exists.
3% reference	300 Paid / 10,000 Free is a useful relationship, but separate direct-paid, enterprise and Free-to-Paid conversion cohorts.

13.3 Growth Command Centre

Panel	Must Show
Today	Registrations, activations, meetings, paid conversions, payment success.
This Week	Free target/actual, Paid target/actual, conversion, campaign performance.
Day-90 Forecast	Projected Free/Paid, variance, confidence.
Required Run Rate	Users/day, users/week, conversions/day/week.
Funnel	Visitor → registration → activation → repeat use → upgrade → payment → entitlement.
Channels	Source, CAC, activation, conversion, retention.
Growth Blockers	Defects/issues directly threatening acquisition, conversion or retention.

Priority Rule
A defect affecting signup, join, invitations, mobile access, payment, subscription, activation, meeting success or retention should be tagged GROWTH BLOCKER when it threatens the 10,000/300 objective.

14. One-Year Connection Freedom Marketing Execution Programme

Marketing operates through weekly Odoo sub-sprints for the full year. The first 13 weeks are integrated with the Day-90 product and commercial programme. Weeks 14–52 retain a weekly objective but are grouped into phases for clarity.

14.1 Marketing Operating Model

Weekly Field	Required
Theme / Audience	Target segment and specific behavioural objective.
Campaign / Content	What is published, demonstrated, emailed, promoted or activated.
Channel	Website, search, social, email, partner, event, direct sales, referral, community.
Offer / CTA	Free registration, meeting creation, demo, webinar, upgrade, partner action.
Targets	Free Users, Paid Users, leads, activation, conversion, retention as applicable.
Economics	Budget, CAC, revenue contribution where measurable.
Evidence	Campaign assets, analytics, registrations, payments, event attendance.
Learning	What changed next week based on evidence.

14.2 First 13 Weeks — Detailed Marketing Sprints

Wk	Dates	Theme	Audience	Actions	Expected Evidence
1	10–16 Aug	Foundation audit	Government, enterprise, communities, existing network	Audit brand/site/channels; define Connection Freedom message hypotheses; establish baseline analytics.	Baseline report; messaging backlog; no vanity targets.
2	17–23 Aug	Segment & funnel design	Priority launch segments	Personas, landing-page wireframes, acquisition/conversion funnel, CTA architecture.	Approved funnel; landing-page requirements.
3	24–30 Aug	Messaging & CRM foundation	Priority launch segments	Connection Freedom messaging house; content calendar; CRM capture and campaign taxonomy.	Message pack; CRM source tracking.
4	31 Aug–6 Sep	Market engine prep	Early adopters	Landing pages, email sequences, social templates, referral design, campaign attribution, demo assets.	Launch-ready assets and tracking.
5	7–13 Sep	Controlled acquisition	Warm network / early adopters	Invite-based acquisition, founder/CEO outreach, controlled social/email, user interviews.	First acquisition cohort and feedback.
6	14–20 Sep	Paid proposition	Activated Free users + prospects	Upgrade messaging, plan comparison, payment trust copy, lead nurture, testimonials.	Initial Paid conversions measurable.
7	21–27 Sep	Connection Freedom launch	Broader market	Launch campaign, demos/webinars, partner/referral activation, enterprise/government proof.	Day-45 market activation; accelerated registrations.

Wk	Dates	Theme	Audience	Actions	Expected Evidence
8	28 Sep–4 Oct	Mobile-led growth	Mobile-first users, communities, professionals	QR/app journey, mobile-focused social, community activation, referral invitations.	Higher mobile registrations/activation.
9	5–11 Oct	Funnel optimisation	All active channels	Analyse drop-offs, retarget non-activated users, improve high-performing channels.	Day-60 run-rate improvement.
10	12–18 Oct	Conversion proof	Activated users, decision makers	Case studies, testimonials, use-case content, targeted upgrade campaign.	Improved Free-to-Paid conversion.
11	19–25 Oct	Partnership scale	Associations, institutions, partners	Partner campaigns, webinars, direct enterprise/government activity, community programmes.	Partner-attributed pipeline/users.
12	26 Oct–1 Nov	Target closing	Highest-performing cohorts	Budget/channel reallocation; referral, reactivation and conversion push.	Maximum projected Day-90 target.
13	2–7 Nov	90-day proof & reset	Market + internal stakeholders	Final push; publish approved proof; channel review; reset Year-1 plan using data.	10,000/300 result; documented channel economics.

14.3 Weeks 14–52 — Weekly Marketing Sprint Calendar

Wk	Dates	Phase	Weekly Theme	Primary Segment	Objective	Primary KPI	Owner
14	08 Nov–14 Nov	Retention & Proof	Activation rescue	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
15	15 Nov–21 Nov	Retention & Proof	First-meeting success	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
16	22 Nov–28 Nov	Retention & Proof	Repeat meeting habit	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
17	29 Nov–05 Dec	Retention & Proof	Webinar adoption	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
18	06 Dec–12 Dec	Retention & Proof	Replay usage	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
19	13 Dec–19 Dec	Retention & Proof	Case study week	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
20	20 Dec–26 Dec	Retention & Proof	Customer story week	Existing users and newly activated cohorts	Increase activation, repeat use and evidence.	Activation/retention/repeat-use	Growth & Ecosystem
21	27 Dec–02 Jan	Sector Penetration	Government use cases	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
22	03 Jan–09 Jan	Sector Penetration	Enterprise collaboration	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
23	10 Jan–16 Jan	Sector Penetration	Education engagement	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
24	17 Jan–23 Jan	Sector Penetration	Media/TV House	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
25	24 Jan–30 Jan	Sector Penetration	Professional associations	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
26	31 Jan–06 Feb	Sector Penetration	SME productivity	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem

Wk	Dates	Phase	Weekly Theme	Primary Segment	Objective	Primary KPI	Owner
27	07 Feb–13 Feb	Sector Penetration	Events & paid webinars	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
28	14 Feb–20 Feb	Sector Penetration	Sector proof consolidation	Named priority sector	Acquire users and proof in a focused vertical.	Segment leads, Free/Paid, CAC	Growth & Ecosystem
29	21 Feb–27 Feb	Partner & Ecosystem Growth	Reseller recruitment	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
30	28 Feb–06 Mar	Partner & Ecosystem Growth	Ambassador activation	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
31	07 Mar–13 Mar	Partner & Ecosystem Growth	Technology partners	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
32	14 Mar–20 Mar	Partner & Ecosystem Growth	Association partnerships	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
33	21 Mar–27 Mar	Partner & Ecosystem Growth	Community leaders	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
34	28 Mar–03 Apr	Partner & Ecosystem Growth	Partner co-marketing	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
35	04 Apr–10 Apr	Partner & Ecosystem Growth	Referral optimisation	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
36	11 Apr–17 Apr	Partner & Ecosystem Growth	Partner performance review	Partners/resellers/communities	Create partner-attributed users, pipeline and reach.	Partner-attributed users/revenue	Growth & Ecosystem
37	18 Apr–24 Apr	Africa & Country Expansion	Country prioritisation	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
38	25 Apr–01 May	Africa & Country Expansion	Country landing pages	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
39	02 May–08 May	Africa & Country Expansion	Local payment readiness	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
40	09 May–15 May	Africa & Country Expansion	Local partner activation	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
41	16 May–22 May	Africa & Country Expansion	Local content/localisation	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
42	23 May–29 May	Africa & Country Expansion	Regional event week	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
43	30 May–05 Jun	Africa & Country Expansion	Country campaign pilot	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
44	06 Jun–12 Jun	Africa & Country Expansion	Regional performance review	Selected country/region	Validate repeatable country expansion mechanics.	Country users, conversion, local partner pipeline	Growth & Ecosystem
45	13 Jun–19 Jun	Scale & Year-2 Preparation	Enterprise expansion	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem
46	20 Jun–26 Jun	Scale & Year-2 Preparation	High-value conversion	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem

Wk	Dates	Phase	Weekly Theme	Primary Segment	Objective	Primary KPI	Owner
47	27 Jun–03 Jul	Scale & Year-2 Preparation	Retention/renewal	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem
48	04 Jul–10 Jul	Scale & Year-2 Preparation	Upsell & add-ons	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem
49	11 Jul–17 Jul	Scale & Year-2 Preparation	Brand equity	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem
50	18 Jul–24 Jul	Scale & Year-2 Preparation	Best-channel scale	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem
51	25 Jul–31 Jul	Scale & Year-2 Preparation	Customer advocacy	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem
52	01 Aug–07 Aug	Scale & Year-2 Preparation	Partner renewal	Highest-value cohorts and channels	Improve recurring revenue, advocacy and next-year readiness.	MRR/ARR, retention, LTV, advocacy	Growth & Ecosystem

FIGURE 14.1 PLACEHOLDER — 52-Week Marketing Roadmap

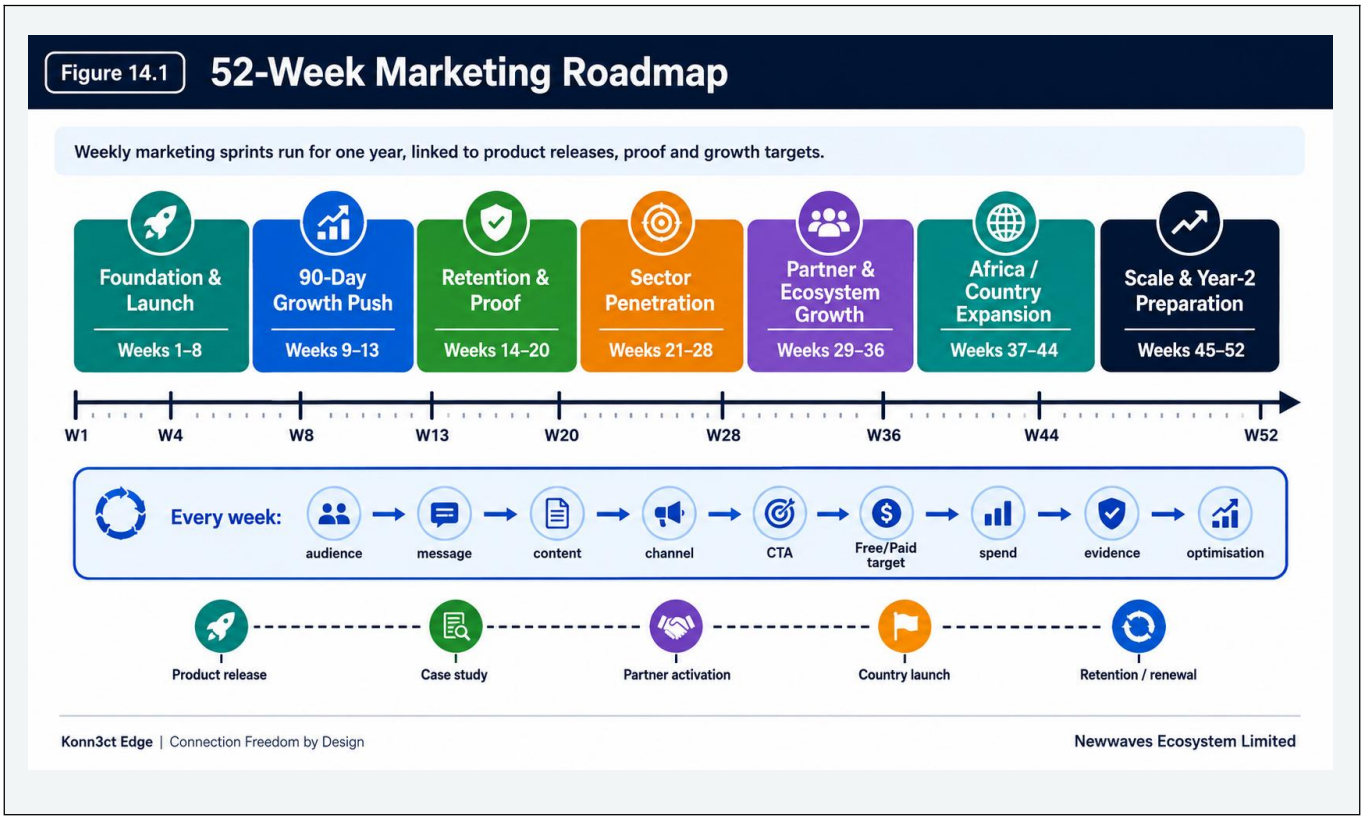


Figure 14.1. 52-Week Marketing Roadmap. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

15. Product and User Experience Execution

The first 90 days should prioritise the minimum sufficient modules required to acquire, activate, convert and retain users. Product sequencing should explicitly distinguish acquisition-critical, conversion-critical, retention-critical and post-90 scale capabilities.

Module	Day-90 Role	Minimum Acceptance
Registration / Authentication	Acquisition critical	Unique legitimate registration, verification, recoverable login, analytics.
Meeting Create/Join/Invite	Acquisition + activation critical	Fast dependable join, shareable invitation, clear host/participant journey.
Audio/Video/Reconnect	Retention critical	Stable media, recovery after transient issues, weak-network behaviour.
Host/Participant Controls	Experience critical	Predictable mute, chat, waiting room, hand raise, reactions, end meeting.
Mobile	Acquisition/retention critical	Reliable Android/iOS core journey, background/foreground recovery, notifications.
Webinar	Growth/commercial enabler	Usable host/attendee separation and event flow.
Recording/Replay	Retention/commercial enabler	Reliable capture, privacy, storage, playback and entitlement.
Free/Paid/Payment/Entitlement	Conversion critical	Automated upgrade → payment → entitlement → receipt → lifecycle.
Analytics	Management critical	Source, activation, meeting, conversion, churn and product-quality telemetry.
Onboarding/Support	Retention critical	First-success guidance, Helpdesk and knowledge path.
Large-room scale	Post-90/enterprise scale	Formal architecture and load-test progression without blocking early market learning.

15.1 Experience-Led Prioritisation

Prioritisation should combine Blueprint importance, Connection Freedom impact, number of users affected, severity, reliability, security, revenue/conversion impact, customer urgency, technical dependency, effort and risk. A visible new feature should not outrank a serious join/audio/payment/reconnect problem merely because it appears more marketable.

16. Mobile Connection Freedom Programme

Mobile is an equal product channel, not a reduced afterthought. Its programme must preserve the hard-won fixes already achieved and build formal regression tests around them.

Quality Area	Required Scenarios
Lifecycle	Launch, foreground/background, PiP where supported, screen lock, app switching.
Media	Mic, camera, Bluetooth, speaker route, camera recovery, audio recovery.
Network	Wi-Fi/mobile transition, weak network, temporary offline, reconnect.
Meeting Controls	Join, host/participant controls, chat, reactions, screen sharing as supported.
Notifications	Meeting/event reminders, in-app notices, reconnect and support cues.
Commercial	Login, plans, payment handoff/entitlement, replay.
Compatibility	Supported Android/iOS versions, low-cost devices, screen sizes.
Observability	Crash monitoring, reconnect telemetry, media-state diagnostics.

Regression Protection

Mobile background/PiP/reconnection improvements already working must be treated as protected regression cases. Any change in media lifecycle code should automatically invoke those scenarios.

17. Technical Architecture and Konn3ct Edge Transformation

The architecture roadmap should transition progressively toward a Kubernetes-native, observable, scalable platform without destabilising the live Version 1 products. Major architecture changes require ADRs, non-production validation and explicit migration/rollback plans.

17.1 Target Architecture Domains

- Control plane: identity, authentication, signalling, WebSockets, chat, polls, presence, host controls, room state, entitlements and session management.
- Media plane: mediasoup SFUs, transports, producers/consumers, audio/video/screenshare, adaptive media, recording streams and large-room sharding.
- Room allocator: policy-driven room placement, node health/capacity awareness and signed allocation.
- Data services: transactional database, cache, queues/events, object storage and analytics pipeline.
- Edge services: web/mobile clients, notifications, payment/subscription, recording/replay, AI services, Odoo integrations and admin dashboards.

FIGURE 17.1 PLACEHOLDER — Kubernetes-Native Control Plane / Media Plane Architecture

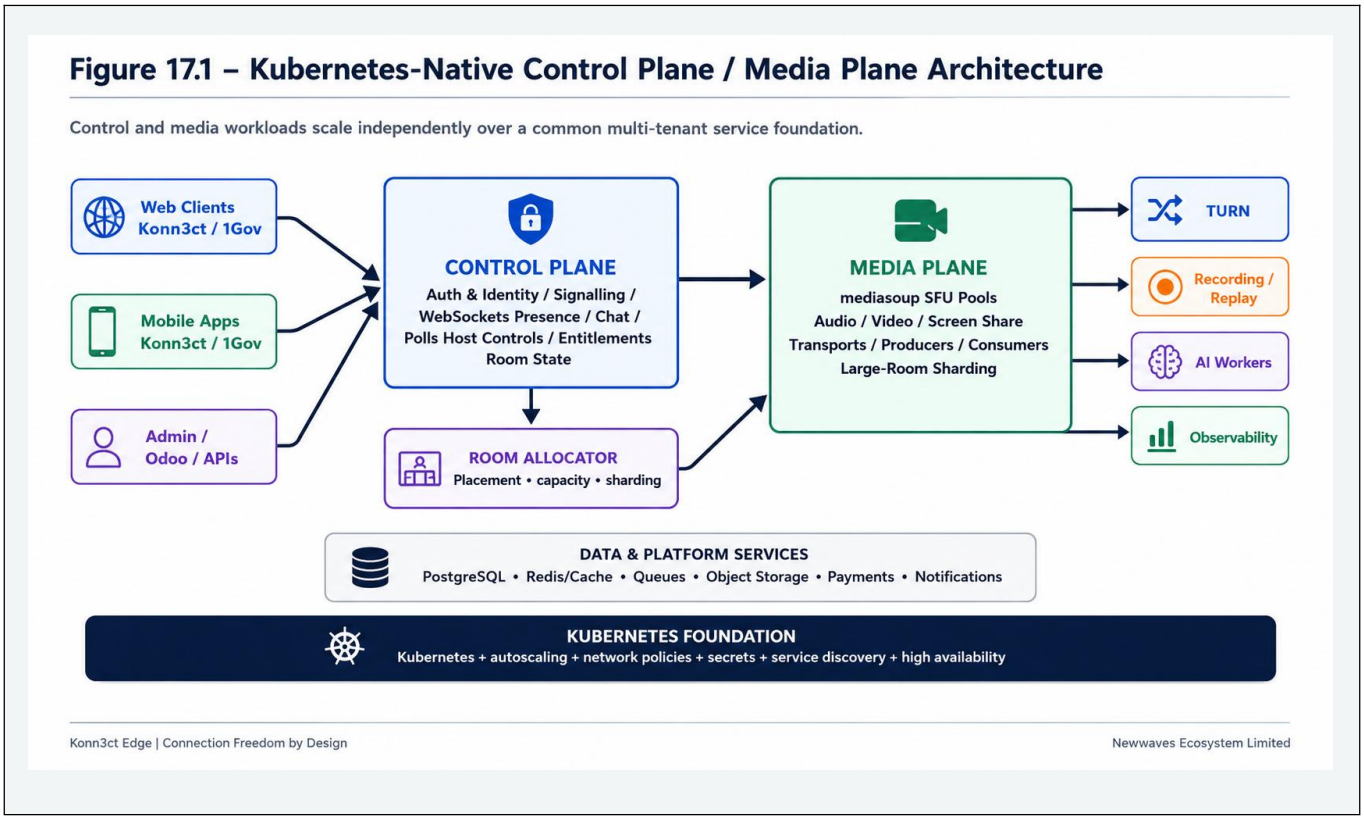


Figure 17.1. Kubernetes-Native Control Plane / Media Plane Architecture. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

18. Kubernetes, Autoscaling and Site Reliability Engineering

18.1 Kubernetes Implementation Sequence

1. Establish non-production cluster and baseline namespaces/policies.
2. Containerise and validate stateless control services.
3. Implement observability, secrets and deployment automation.
4. Introduce room allocator and media-node registration.
5. Move selected media workloads into controlled node pools.
6. Implement metrics-driven HPA/custom autoscaling and overload protection.

7. Run repeatable load/failover tests before production reliance.
8. Progressively adopt production and customer-specific deployment standards.

18.2 Autoscaling Signals

Service	Primary Signals
Web/API	CPU/memory, requests, latency, error rate.
Signalling	WebSocket connections, event-loop lag, message throughput, memory.
Media/SFU	Rooms, participants, transports, producers, consumers, bitrate, node bandwidth, CPU/memory.
Recording	Active jobs, queue depth, encode/upload time.
AI	Transcription/summarisation queue, latency, accelerator/CPU utilisation.
Room Allocator	Healthy node capacity, allocation failure, geographic demand.
Database/Cache/Queue	Latency, connections, hit rate, queue depth, replication/health.

CPU-only autoscaling is insufficient for media workloads. Capacity policy should include baseline, burst, maximum tested capacity, admission control, graceful degradation, scale-up/down thresholds and cost limits.

18.3 SRE Targets

SLI/SLO	Initial Governance Use
Availability	Service uptime and planned maintenance accounting.
Join success / join latency	Core Connection Freedom measure.
Audio/video success	Media quality gate.
Reconnect success	Continuity measure.
Recording/replay success	Content reliability.
Payment success	Commercial reliability.
Crash-free mobile sessions	Mobile quality.
Incident recovery time	Operational maturity.
Error budget	Release pacing when reliability falls below approved target.

19. DevOps, DevSecOps and CI/CD

The pipeline should convert every change into auditable evidence. A build should stop automatically on agreed critical failures rather than depending on manual memory.

Pipeline Stage	Controls
Commit/PR	Branch naming, requirement ID, code review, protected branches.
Build	Formatting, linting, type checks, unit tests.
Security/Compliance	Secret scan, SAST, dependency/SCA, licence check, SBOM, container/IaC scan.
Integration	API/integration tests, migration validation, contract tests.
Experience	Browser/mobile/e2e tests, key Connection Freedom regression pack.
Performance	Targeted load/performance checks for affected services.
Package	Signed/versioned artefact, release notes, provenance.
Deploy	Staged/canary/blue-green where appropriate, environment approval, database migration guard.

Pipeline Stage	Controls
Verify	Smoke tests, telemetry check, rollback threshold, Odoo release/deployment update.

FIGURE 19.1 PLACEHOLDER — DevSecOps Release Pipeline

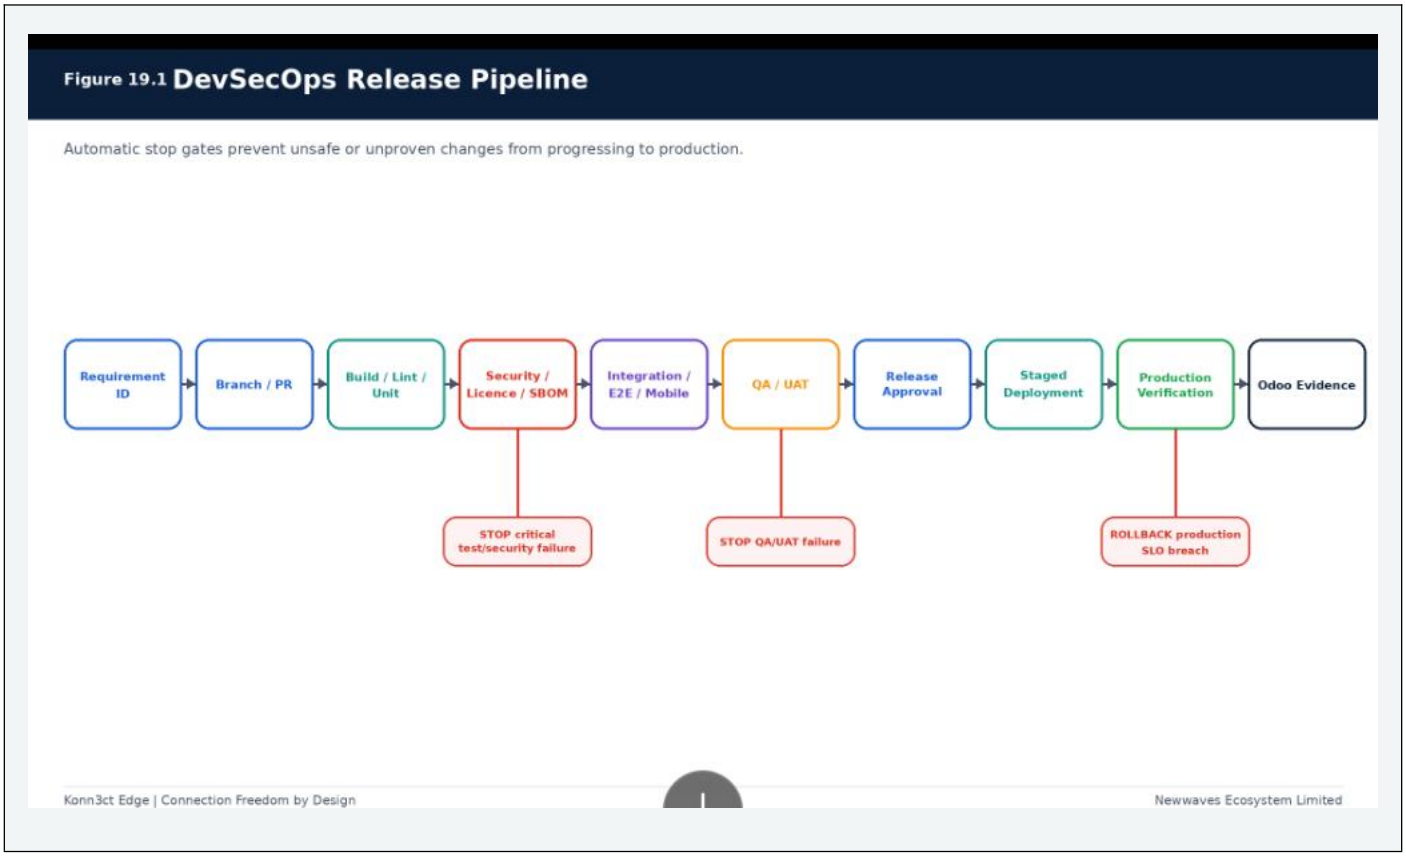


Figure 19.1. DevSecOps Release Pipeline. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

20. Quality Assurance and Release Certification

QA certifies both technical correctness and experience correctness. The release gate should prove that intended users can successfully complete the relevant journey under realistic devices, browsers and network conditions.

Test Family	Examples
Functional	Meeting/webinar controls, chat, polls, reactions, recording, replay, payment.
Media	Audio, video, screenshare, active speaker, reconnect, device switching.
Mobile	Lifecycle, PiP/background, permissions, crash/recovery, network switching.
Compatibility	Supported OS/versions, browsers/versions, device classes.
Performance	Load, stress, endurance, large-room, resource saturation.
Resilience	Network degradation, service restart, failover, recovery.
Security/Privacy	Authentication, authorisation, recording/privacy, API, mobile, Kubernetes.
Commercial	Free/Paid, payment, subscription, entitlement, renewal/cancellation.
White Label	Konn3ct and 1Gov compatibility/regression.
Production	Post-deploy smoke and telemetry validation.

20.1 Required Personas

- First-time user; ordinary business user; IT-illiterate user; low-cost-device user; weak-network user; mobile-only user; guest participant; host; co-host; webinar attendee/presenter; paid-event attendee; enterprise administrator.

FIGURE 20.1 PLACEHOLDER — QA / Connection Freedom Certification Gate

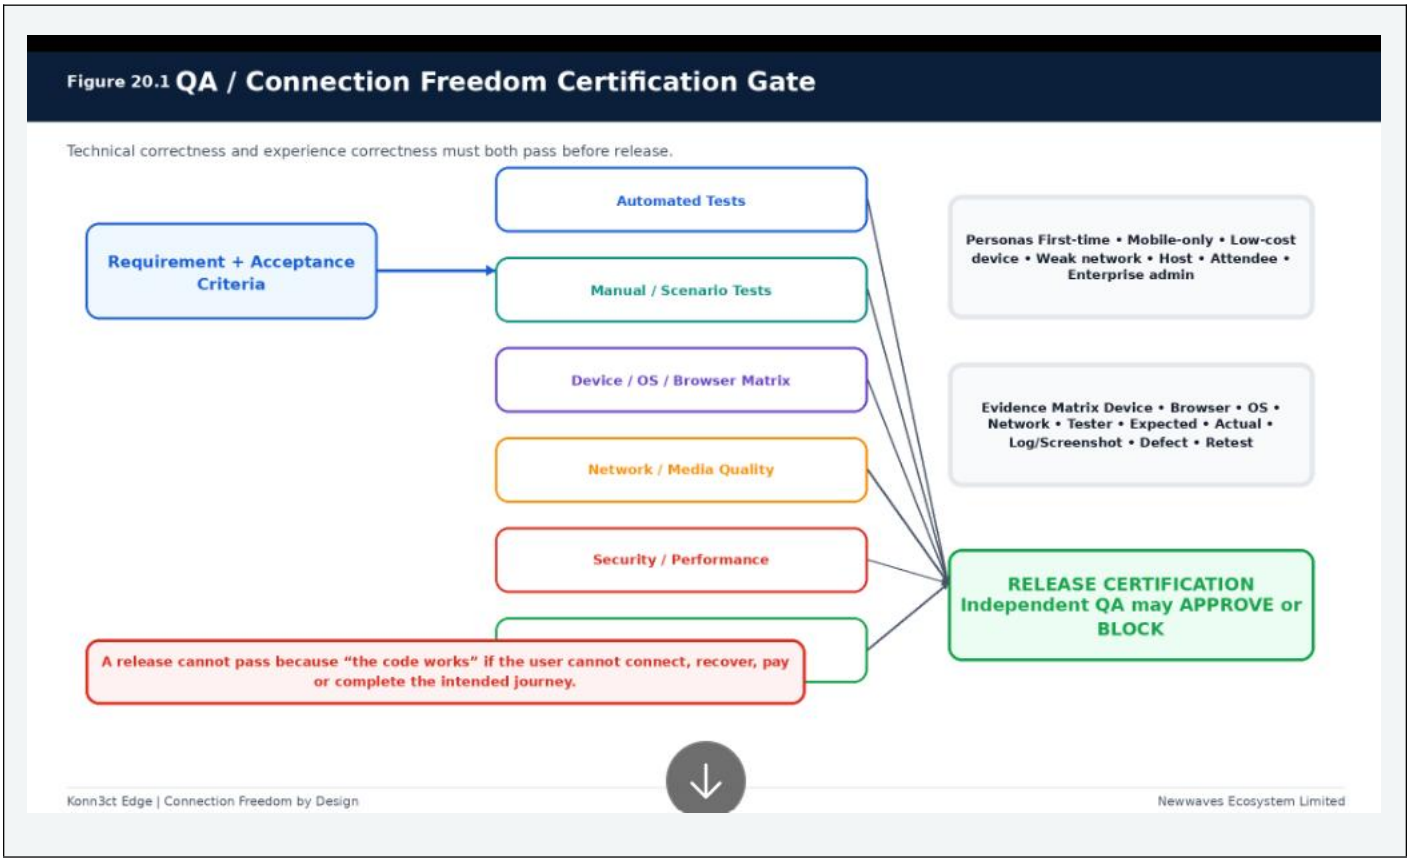


Figure 20.1. QA / Connection Freedom Certification Gate. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

21. TrustLock™, Cybersecurity, Privacy and Licensing

21.1 Security-by-Design Gates

Gate	Minimum Control
Concept/Requirement	Data classification, misuse/abuse and privacy implications.
Architecture	Threat model, trust boundaries, tenant isolation, secrets and logging.
Development	Secure coding, dependency provenance, least privilege.
Build	SAST/SCA/secret/container/IaC scans.
QA	AuthZ, data exposure, API/mobile/WebRTC/Kubernetes tests.
Release	Critical findings resolved or formally accepted by authorised human.
Operations	Monitoring, vulnerability management, incident response, access recertification.

21.2 Software Licensing and SBOM

- Identify every open-source/commercial library, codec, font, icon, AI model, API, Odoo module and infrastructure dependency.
- Define permitted, restricted and prohibited licence classes with legal-review triggers.
- Generate a Software Bill of Materials for each release.

- Track attribution, redistribution/source-disclosure risk, renewal dates, usage limits and end-of-life dependencies.
- Keep customer subscription entitlements separate from development licence compliance, but reconcile both through Odoo governance.

22. Commercial Model and Revenue Operations

Commercial modules must be implemented early enough to support the Day-90 Paid target. The ordinary user upgrade journey should be automated end-to-end wherever practical.

FIGURE 22.1 PLACEHOLDER — Free-to-Paid Conversion and Entitlement Flow

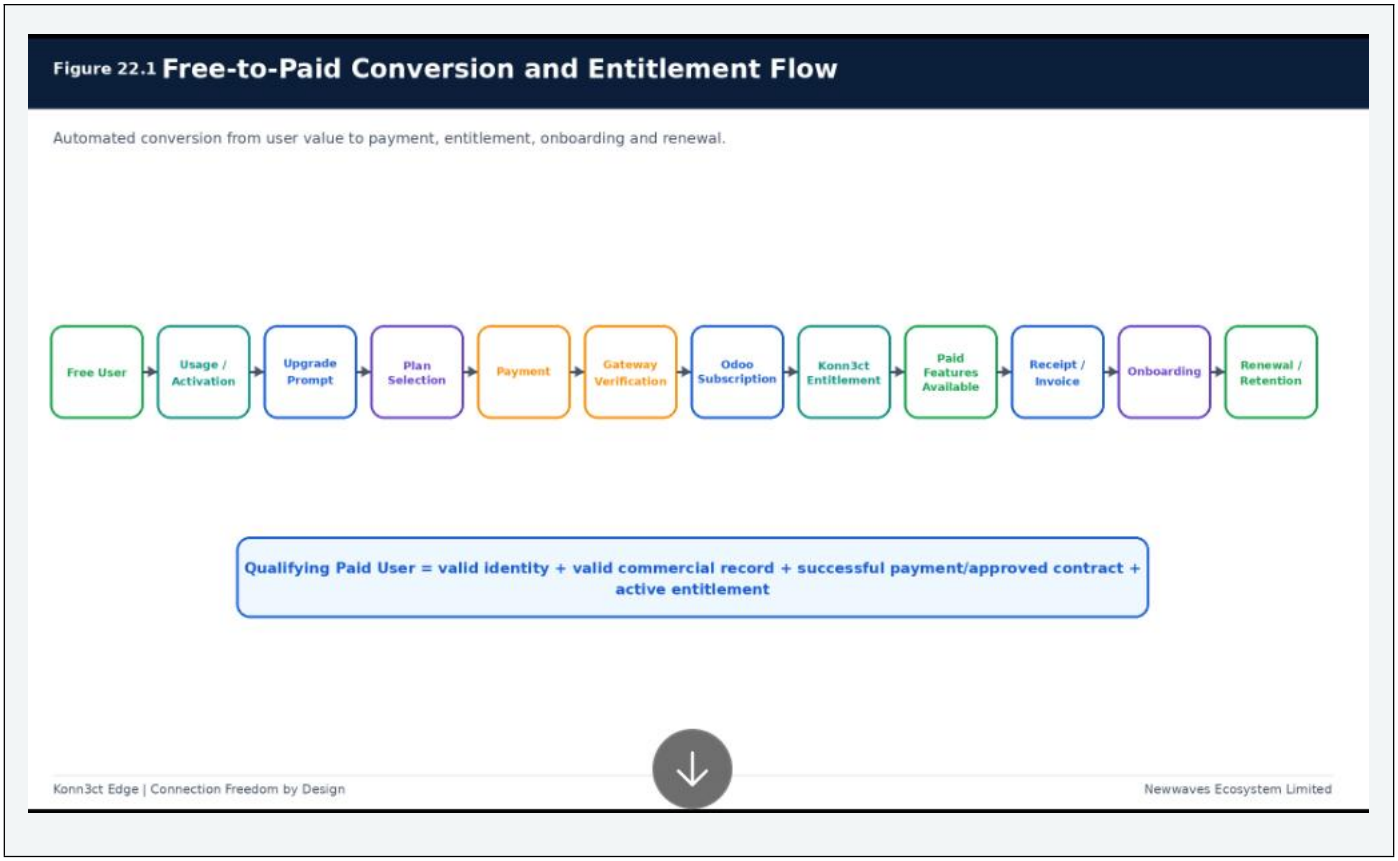


Figure 22.1. Free-to-Paid Conversion and Entitlement Flow. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

Commercial Capability	Day-90 Requirement
Free Plan	Clear value, limits and frictionless activation.
Paid Plan	Approved price/value proposition with reliable entitlement.
Payments	At least primary payment path stable; reconcile status and failure.
Subscriptions	Activation, renewal, upgrade, downgrade, cancellation, grace/suspension rules.
Entitlements	Technical access always consistent with approved plan/payment/contract.
Receipts/Invoices	Automatic record and customer communication.
Analytics	Conversion, payment success, MRR/ARR, churn, source and cohort.
Enterprise/1Gov	Contractual entitlement handled without distorting individual Free→Paid metrics.

23. Growth, Marketing Technology and Product-Led Acquisition

The product itself must create a growth loop: hosts invite participants, participants experience Konn3ct, some register and host their own sessions, and qualified users upgrade. Marketing should amplify this loop rather than rely only on paid media.

FIGURE 23.1 PLACEHOLDER — Konn3ct Growth Flywheel

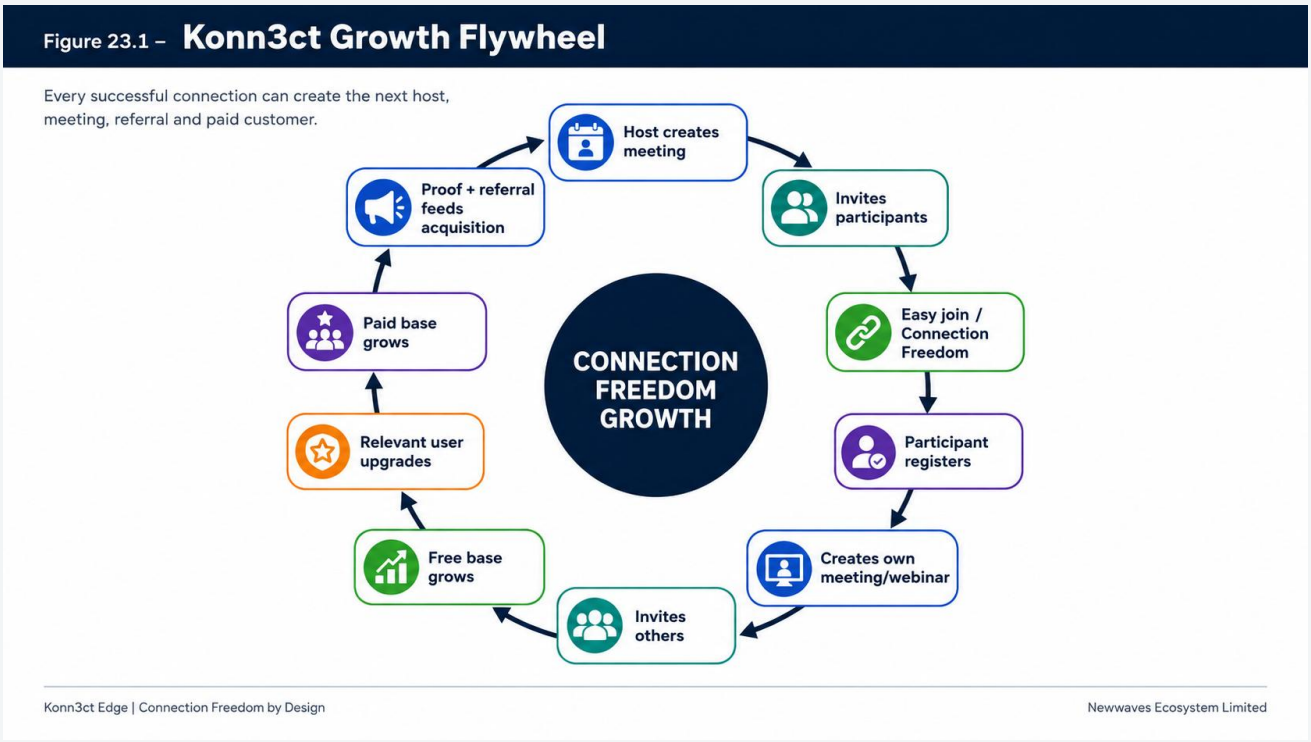


Figure 23.1. Konn3ct Growth Flywheel. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

23.1 Growth Blocker Triage

Any defect or friction affecting registration, join, invitations, mobile access, payment, subscription, activation, meeting success or repeat use should be linked to a funnel stage and prioritised according to lost-user/revenue risk.

24. Customer Success, Support and Feedback-to-Engineering

Customer Success should protect the Connection Freedom promise. The objective is not simply to close tickets but to restore the customer's ability to connect and prevent recurrence.

Lifecycle Moment	Operational Measure
Onboarding	Time to first successful meeting/webinar.
Activation	Share of new users reaching approved activation event.
Support	Time to restore experience; first-contact resolution; recurrence.
Health	Usage, quality, support, payment and sentiment signals.
Retention	Repeat use, renewal, churn risk and intervention.
Expansion	Upgrade, additional hosts/capabilities, enterprise adoption.
Voice of Customer	Feedback classified into defect, enhancement, training/support or policy.

FIGURE 24.1 PLACEHOLDER — Support → Product → QA Feedback Loop

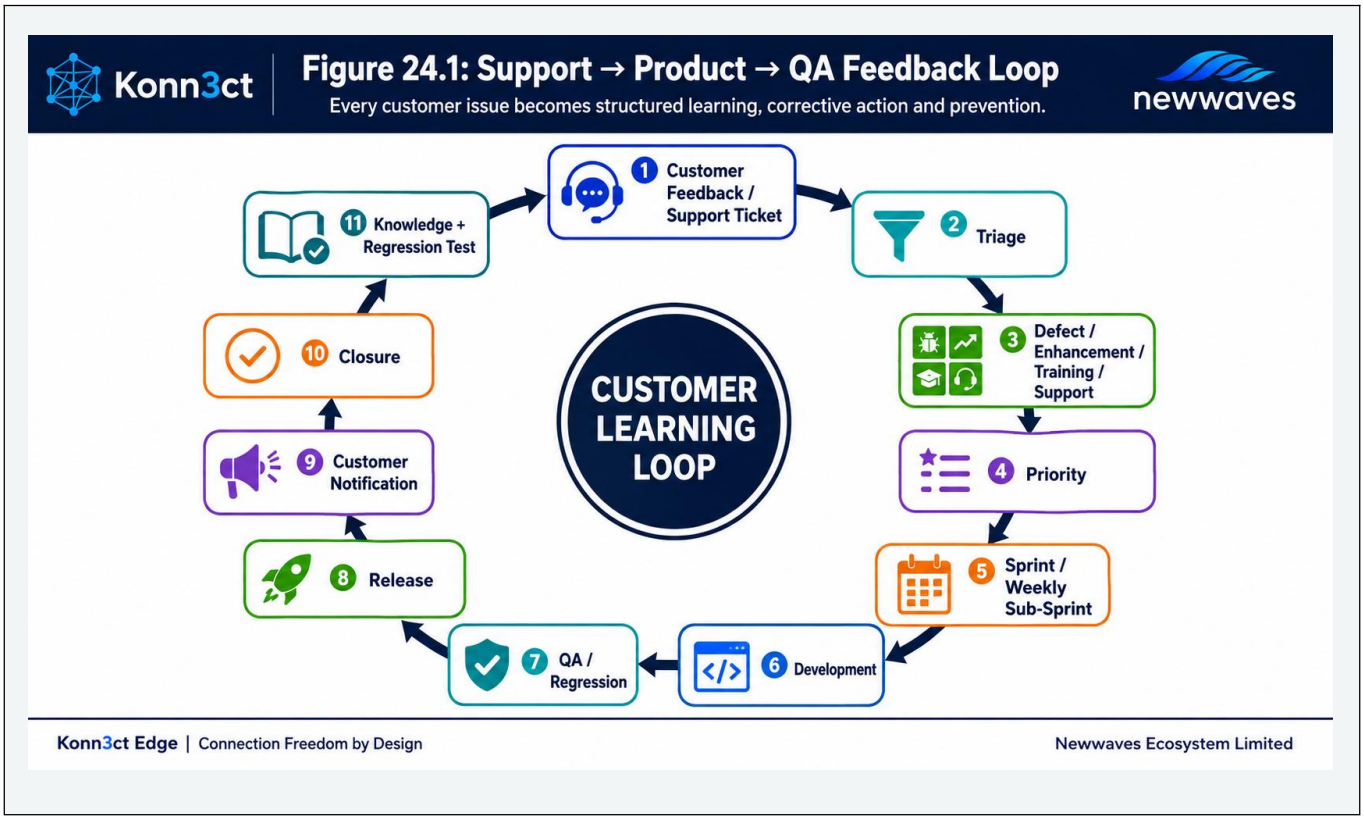


Figure 24.1. Support → Product → QA Feedback Loop. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

25. Dashboards, KPIs and Management Intelligence

25.1 CEO Dashboard

- Blueprint/phase completion and weekly sprint score.
- 1Gov, Konn3ct V1 and Edge track health.
- Connection Freedom Index and core quality measures.
- Free Users, Paid Users, conversion, MRR/ARR/revenue and Day-90 forecast.
- Release readiness, critical defects, security/licensing risks and incidents.
- Budget/staffing, major dependencies and decisions required.

25.2 Growth & Ecosystem Dashboard

- Roadmap/UX, acquisition funnel, campaign/channel performance, Free/Paid targets, conversion, onboarding, retention, churn, partner contribution, country/sector performance.

25.3 Technology & Business Operations Dashboard

- Development/PR/build/test status, defect aging, releases, Kubernetes health, autoscaling/capacity, SRE, infrastructure cost, security findings, licence risks, incidents and technical debt.

25.4 PMO Dashboard

- Portfolio/project status, weekly sprint scores, milestone variance, resource load, dependencies, risks/issues/decisions, overdue evidence and carry-over.

FIGURE 25.1 PLACEHOLDER — Executive Dashboard Architecture

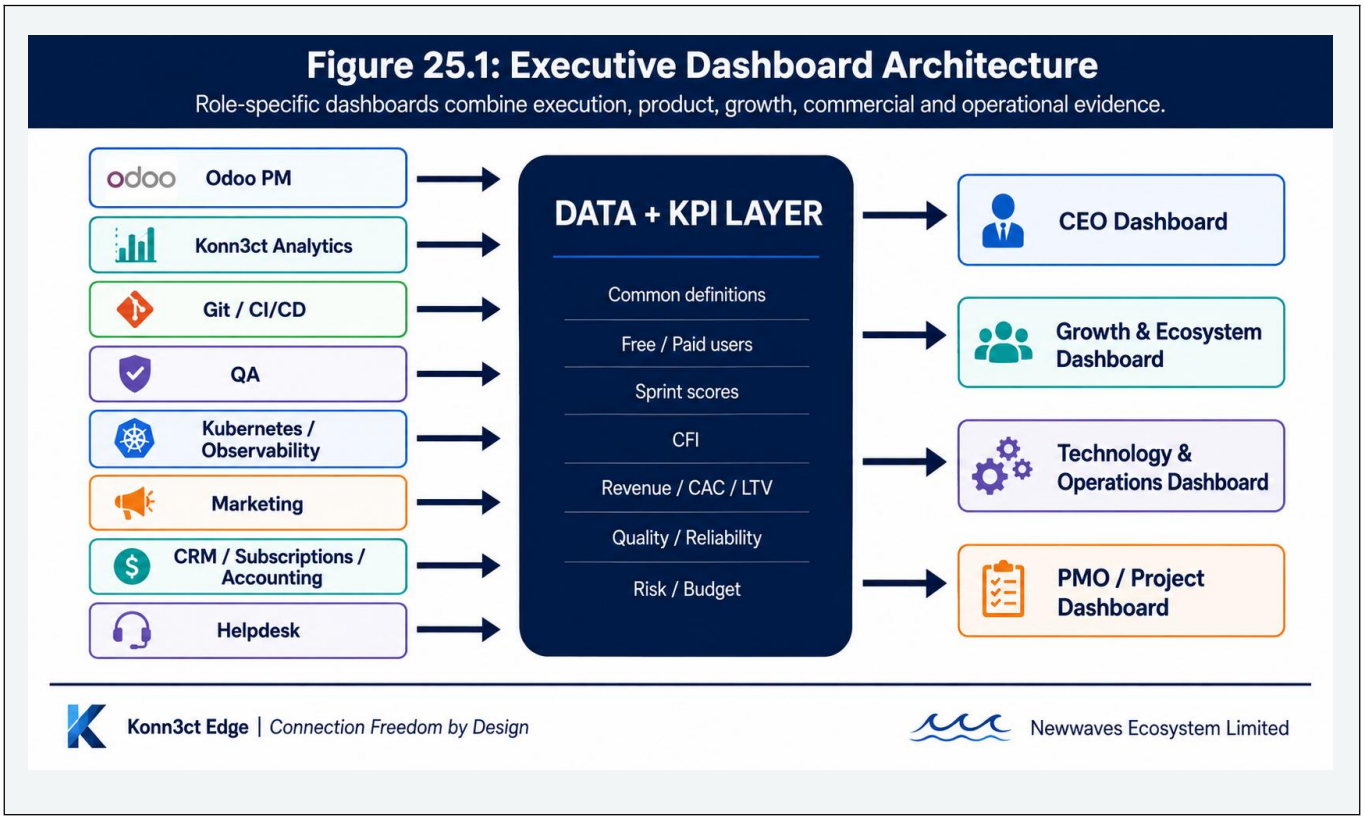


Figure 25.1. Executive Dashboard Architecture. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

26. Risk Management

Risk	Probability	Impact	Primary Control	Owner
Technical regression	High	High	Regression suite, release rings, protected branches.	Technology & Business Operations
1Gov disruption	Med	High	Tenant compatibility, staging/acceptance, customer change control.	Technology & Business Operations
PM module misses Day 30	Med	High	Use MVP acceptance gate, daily integration tracking, parallel work.	Technology & Business Operations
10k/300 run rate below target	High	High	Day-45 activation, weekly forecast, channel/product optimisation.	Growth & Ecosystem
Mobile instability	Med	High	Protected regression scenarios, device matrix, crash/reconnect telemetry.	Mobile Lead
AI agent causes unsafe change	Low/Med	High	Restricted permissions, human approvals, audit, sandbox.	Technology & Business Operations
Kubernetes migration destabilises product	Med	High	Progressive adoption, non-prod validation, rollback.	DevOps/SRE
Cybersecurity vulnerability	Med	High	TrustLock gates, scanning, pentest, incident response.	Security Lead
Licensing exposure	Low/Med	High	SBOM, licence policy, approval before dependency use.	Licensing/Security

Risk	Probability	Impact	Primary Control	Owner
Marketing claims exceed evidence	Med	Med/High	Approved proof, Product/QA signoff, 1Gov confidentiality control.	Growth & Ecosystem
Insufficient internal capability	Med	High	Capability-transfer field in every sprint; targeted external support.	Both Managers
White-label fragmentation	Med	High	Common-core governance, config-first, extension approval.	Architecture Review Board

27. Internal Capability and Culture Transformation

Konn3ct Edge and 1Gov are training environments for Newwaves itself. Every sprint should leave the organisation more capable of repeating the work without dependence on individual memory or external intervention.

Level	Definition
1 Ad Hoc	Work depends on individual effort and informal memory.
2 Repeatable	Basic process exists and can be repeated with guidance.
3 Defined	Documented standard process and ownership.
4 Measured	Performance is instrumented and governed by KPIs.
5 Optimised	Process is automated, continuously improved and resilient to staff changes.

27.1 Functions to Score

- Project/portfolio management; product/requirements; UX; engineering/Git; AI-assisted development; QA; DevOps/Kubernetes/SRE; cybersecurity; Odoo; mobile; marketing/growth; commercial operations; customer success/support; analytics.

Measure at Day 1, Day 30, Day 90, Day 180 and Day 365. Every weekly sub-sprint must record a capability-transfer outcome: what was learned, by whom, how it is documented and whether the team can repeat it.

28. 18-Month Blueprint Roadmap

Phase	Period	Theme	Primary Outcomes
0	10 Aug–6 Sep 2026	Mobilisation	Governance, PM system, baselines, tools, first sprints.
1	10 Aug–31 Oct 2026	Stable Connection	Core reliability, QA, monitoring, mobile and production blockers.
2	7 Sep–31 Dec 2026	Connection Freedom Foundation	Kubernetes foundation, common core, AI orchestration, traceability, TrustLock baseline.
3	2 Nov 2026–31 Mar 2027	Marketable Konn3ct Edge	Improved web/mobile, meetings/webinars, recording/replay, payments, onboarding, AI essentials.
4	4 Jan–30 Jun 2027	Freedom to Grow	Free/Paid scale, marketing automation, CRM, customer success, partners, monetisation.
5	1 Mar–30 Sep 2027	Freedom at Scale	Large rooms, sharding, autoscaling, SRE, enterprise/private cloud, advanced security.
6	1 Jul 2027–31 Jan 2028	Connection Freedom Everywhere	Country expansion, partners, localisation, local payments, repeatable white-label operations.

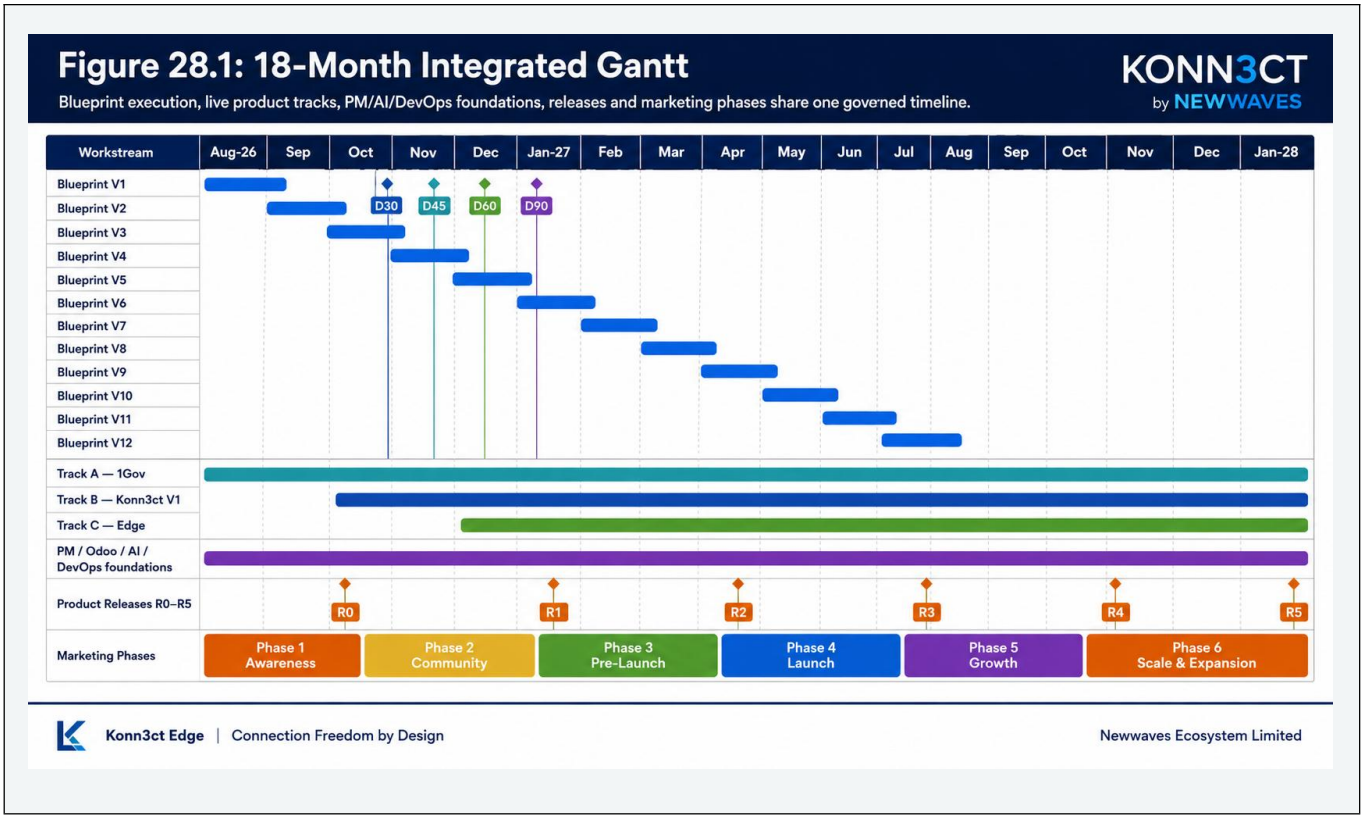


FIGURE 28.1 PLACEHOLDER — 18-Month Integrated Gantt Placeholder

Figure 28.1. 18-Month Integrated Gantt Placeholder. Final artwork to be inserted in the approved Newwaves/Konn3ct visual system.

29. Immediate Action — Monday, 10 August 2026

Role	Day-1 Actions
CEO	Approve programme charter, 30/90-day commitments, two-manager accountability, PM as execution system, Day-90 growth metrics and escalation rules.
Growth & Ecosystem Manager	Confirm priority user segments, current Free/Paid baseline, Connection Freedom positioning, product/growth backlog and Day-45 market gate.
Technology & Business Operations Manager	Freeze uncontrolled changes; establish baseline builds; launch PM/Odoo, repository, QA, integration and environment workstreams.
PM/Odoo Team	Create portfolio/programme/projects, users, stages, first sprint/sub-sprint, risk/issue/decision registers.
Product/UX	Map critical journeys and top Connection Freedom barriers for Konn3ct and 1Gov.
Engineering	Tag current build, establish defect baseline, link work to requirement IDs, protect working fixes.
Mobile	Freeze known-good reconnect/background baseline and define regression pack.
QA	Create quality gate, severity rules, current test inventory and evidence standard.
DevOps	Inventory environments, CI/CD, secrets, monitoring and Kubernetes readiness.
Marketing	Audit website/channels/assets, baseline analytics and draft Connection Freedom message hypotheses.
Customer Success	Consolidate 1Gov and Konn3ct feedback/support issues and onboarding gaps.

Role	Day-1 Actions
ChatGPT	Use this strategy as governing context; create initial PM/Product/Technology/Growth review prompts.
Antigravity	Operate only on approved work orders and restricted branches; no uncontrolled production actions.

29.1 First 20 Management Actions

1. Approve the programme charter and this strategy as governing baseline.
2. Confirm Day-30 PM and Day-90 10,000/300 targets.
3. Confirm Growth & Ecosystem and Technology & Business Operations decision rights.
4. Create Konn3ct Edge portfolio/programme and 1Gov/Konn3ct projects in Odoo.
5. Record current qualifying Free/Paid user baselines.
6. Tag production and test baselines in source control.
7. Create the common-core gap register.
8. Freeze unapproved production changes.
9. Approve Week-1 and Week-2 weekly sub-sprints.
10. Establish QA independence and severity rules.
11. Approve system-of-record matrix.
12. Approve initial ChatGPT workspaces and data boundaries.
13. Approve Antigravity autonomy limits.
14. Approve CI/CD and security-gate minimums.
15. Approve initial Kubernetes migration scope.
16. Approve Connection Freedom Index baseline design.
17. Approve Day-45 market activation criteria.
18. Approve marketing attribution taxonomy and launch segments.
19. Approve customer/1Gov confidentiality rules for case-study use.
20. Schedule Friday evidence review and weekly CEO command report.

29.2 First 50 Operational Setup Tasks

#	Operational Setup Task
1	Create Odoo Portfolio: Konn3ct Edge Transformation.
2	Create Programme: Konn3ct Edge 2026–2028.
3	Create Project: 1Gov V1 Production & Customer Continuity.
4	Create Project: Konn3ct V1 Stabilisation & Market Activation.
5	Create Project: Konn3ct Edge Common Core Transformation.
6	Create PM Execution Control System implementation project.
7	Create workstreams for Product/UX, Web, Backend, Mobile, Media, DevOps, QA, Security, Commercial, Marketing, Customer Success.
8	Configure user roles and security groups.
9	Configure customer portal isolation.
10	Create Blueprint Volume master data.

#	Operational Setup Task
11	Create Connection Freedom CF-1..CF-6 master data mappings.

#	Operational Setup Task
12	Create requirement ID sequence.
13	Create sprint and weekly sub-sprint sequence.
14	Create defect/test/release/deployment IDs.
15	Create risk, issue and decision registers.
16	Create architecture decision register.
17	Create document-control register.
18	Create first CEO dashboard.
19	Create manager dashboards.
20	Create weekly sprint score calculation.

#	Operational Setup Task
21	Create Day-90 Growth Command Centre fields.
22	Capture current Free/Paid baseline.
23	Capture current Konn3ct build/version.
24	Capture current 1Gov build/version.
25	Inventory repositories and branches.
26	Inventory environments/secrets.
27	Inventory automated tests.
28	Inventory manual test cases.
29	Inventory critical defects.
30	Create regression-protected mobile scenarios.

#	Operational Setup Task
31	Create 1Gov → Edge Learning Register.
32	Create Konn3ct V1 → Edge Gap Register.
33	Create common-core candidate register.
34	Configure Git requirement-ID conventions.
35	Configure CI callback design.
36	Configure build/test evidence ingestion.
37	Configure failed-build/failed-test defect automation.
38	Create ChatGPT Strategy Partner workspace/context.
39	Create Product/UX AI workspace.
40	Create Technology/Architecture AI workspace.

#	Operational Setup Task
41	Create QA/Security AI workspace.
42	Create Growth/Marketing AI workspace.
43	Define Antigravity work-order template.
44	Restrict Antigravity repository/branch permissions.

#	Operational Setup Task
45	Inventory Kubernetes readiness and target services.
46	Set observability baseline.
47	Create website/marketing channel audit.
48	Create launch segment/persona shortlist.
49	Define Day-45 market activation checklist.
50	Schedule Friday demo/evidence review and Monday commitment cadence.

30. First Two-Week Sprint and Weekly Sub-Sprints

30.1 Sprint 1 — 10–23 August 2026

Sprint Goal: Establish execution control and trusted baselines while removing the first barriers to a measurable Konn3ct acquisition journey.

Weekly Sub-Sprint	Outcome	Owner(s)	Acceptance Evidence
Week 1: 10–16 Aug	PM skeleton live; Konn3ct/1Gov baselines; governance and initial dashboards; growth baseline.	Both Managers + PMO	Projects created; roles/RACI; baseline reports; first Friday score; source-control tags.
Week 2: 17–23 Aug	Requirements/QA/traceability workflow live; critical entry journey specified; Free/Paid product definition.	PMO + Product + QA + Engineering	Approved requirement flow; IDs; test/defect flow; registration/join backlog; approved Free/Paid definition.

30.2 Remaining 90-Day Biweekly Sprints

Sprint	Weeks	Primary Goal
Sprint 2	3–4	Integrate toolchain, stabilise core reliability, prepare market engine.
Sprint 3	5–6	PM go-live, controlled acquisition, paid-conversion technical path.
Sprint 4	7–8	Day-45 market activation and mobile-led growth.
Sprint 5	9–10	Day-60 growth engine and conversion optimisation.
Sprint 6	11–12	Platform scale foundation and target-closing growth sprint.
Gate Week	13	Integrated Day-90 product, growth, QA, security and capability review.

31. Weekly CEO Command Report Template

Section	Content
Overall Status	Green / Amber / Red with one-sentence rationale.
Weekly Sprint Score	Overall and by workstream.
What We Promised	Committed measurable outcomes.
What We Delivered	Accepted outcomes with evidence.

Section	Content
What We Did Not Deliver	Missed commitments and root cause.
Decisions Required	Specific CEO decisions with deadline/impact.
1Gov Status	Customer, release, support, risks.
Konn3ct V1 Status	Stability, testing, release, adoption.
Edge Transformation	Architecture/common-core/PM/AI progress.
Connection Freedom	CFI, major user barriers and improvements.
Growth	Free/Paid actual vs target, forecast and required run rate.
Marketing	Best/worst channels, CAC, campaign outcome.
Quality/Security	Critical defects, release blockers, vulnerabilities.
Budget/Capacity	Material variance and staffing constraints.
Next Week	Approved commitments and major risks.

32. Definition of Done and Production Readiness

A feature is not complete because code was written. Definition of Done must be evidence-based and include the applicable items below.

- Blueprint and Connection Freedom alignment approved.
- UX/user journey and acceptance criteria approved.
- Code complete and reviewed.
- Automated tests and relevant regression tests pass.
- Manual QA/e2e/device/network scenarios pass as applicable.
- Security/privacy/licensing checks complete.
- Documentation and support knowledge updated.
- Monitoring/telemetry implemented.
- Commercial/marketing/customer-success configuration prepared where relevant.
- UAT/product acceptance complete.
- Release and rollback plan approved.
- Production verification completed after deployment.
- Evidence attached in Odoo and KPI owner assigned.

32.1 Production Readiness Checklist

Area	Gate
Scope	Release scope frozen and traced to requirements.
Quality	No unresolved critical release blockers; approved high-severity risk position.
Security	Critical findings resolved/accepted by authorised human.
Performance	Relevant performance/capacity tests passed.
Data/Migration	Migration/rollback verified and backed up.
Operations	Monitoring, alerting, runbook and owner ready.
Support	Helpdesk/knowledge/training ready.
Marketing	Claims match proven capability; customer communication ready.
Tenant Impact	1Gov/white-label compatibility assessed.
Approvals	QA, Product, Technology and required executive approvals recorded.

33. Ongoing Strategy Governance and ChatGPT Review Cycle

This document should be supplied to ChatGPT as the principal strategic reference for future Konn3ct Edge work. ChatGPT should identify conflicts, trade-offs and deviations rather than silently abandoning approved principles.

Cadence	Input Pack	Expected Strategy Partner Output
Weekly	Sprint results, Free/Paid trajectory, defects, releases, marketing, customer feedback, risks.	Strategic interpretation, major concerns, priorities, decisions, next-sprint focus.
Monthly	Programme dashboard, architecture/commercial changes, budget, capability maturity.	Strategy variance review and recommended changes.
Quarterly	Blueprint completion, market evidence, competitive context, organisation/capability.	Formal strategy refresh recommendations.
Major Decision	Decision record and supporting analysis.	Options, implications, recommendation and Blueprint/Connection Freedom impact.

33.1 Strategy Partner Review Questions

1. Which Blueprint objective does this support?
2. Which Connection Freedom outcome does it support?
3. Does it improve user experience or remove friction?
4. Does it protect 1Gov continuity?
5. Can existing Konn3ct V1 capability be reused?
6. Does it strengthen common core or create fragmentation?
7. Does it contribute to Free User acquisition, Paid conversion, retention or revenue?
8. What QA/security/licensing evidence is required?
9. What does it cost and what technical debt does it create?
10. Is it measurable in Odoo and who owns the outcome?
11. What should happen next and by when?

34. Newwaves Konn3ct Edge Execution Command Sheet

Standing Weekly Executive Summary

The command sheet should fit within two pages and be generated from Odoo. It is not a replacement for detailed records; it is the CEO's five-minute management view.

Command Area	Current-Week Requirement
Strategic Priority	One primary programme objective and why it matters now.
1Gov	Current customer/release/support state.
Konn3ct V1	Current test/stabilisation/market state.
Edge Transformation	Common-core/architecture/PM/AI progress.
Weekly Outcomes	Committed vs accepted results.
Free/Paid	Weekly and cumulative target/actual, Day-90 forecast.
Connection Freedom	CFI and top three user barriers.
Quality	Critical defects and release blockers.
Marketing	This week's theme, best channel, spend and conversion.
Customer	Top feedback/support themes.

Command Area	Current-Week Requirement
Risks/Blockers	Only material items needing attention.
Decisions	Named decision, owner and deadline.
Next Week	Proposed commitments and resource implications.

Appendix A. Diagram Placeholder Register

Figure	Title	Purpose
C1	Cover Strategic Visual	Connection Freedom + six freedoms + enabling layers + execution system.
1.1	Konn3ct Edge Strategy Architecture	Whole operating system.
2.1	Three-Track Execution Model	1Gov / Konn3ct V1 / Edge convergence.
3.1	Connection Freedom Strategic Model	Doctrine and enabling layers.
4.1	CEO / Two-Manager Governance	Organisation and management.
5.1	Execution Control Architecture	Odoo PM hierarchy and lifecycle.
6.1	30-Day PM Roadmap	PM/integration go-live.
7.1	People–Process–Tools Integration	Systems integration.
8.1	ChatGPT–Odoo–Antigravity	AI orchestration.
10.1	Common-Core Convergence	White-label governance and release rings.
11.1	Blueprint → Outcome Traceability	End-to-end traceability.
12.1	13-Week Roadmap	First 90 days.
14.1	52-Week Marketing Roadmap	Year-one marketing cadence.
17.1	Kubernetes Architecture	Control/media plane target.
19.1	DevSecOps Pipeline	Release gates.
20.1	QA Certification Gate	Independent quality model.
22.1	Free-to-Paid Flow	Commercial conversion.
23.1	Growth Flywheel	Product-led acquisition.
24.1	Support-to-Product Loop	VOC feedback.
25.1	Dashboard Architecture	Management intelligence.
28.1	18-Month Gantt	Blueprint roadmap.

Appendix B. Blueprint-to-Execution Mapping

Volume	Execution Focus	Lead	Primary Timing
V1 Brand & Strategy	Connection Freedom positioning, messaging, brand governance	Growth & Ecosystem	Aug–Oct 2026; governance ongoing
V2 Marketing & GTM	52-week campaigns, funnels, launch, acquisition	Growth & Ecosystem	Aug 2026–Aug 2027 weekly
V3 Product Strategy	Roadmap, modules, requirements, UX	Growth & Ecosystem	Aug 2026–Mar 2027; ongoing roadmap
V4 Mobile & Multi-Platform	Mobile quality, cross-device journeys	Joint	Aug 2026–Jun 2027; ongoing releases
V5 Hypergrowth & Automation	Odoo-first automation, AI growth, international funnel	Growth & Ecosystem	Jan 2027 onward; early foundations in 90 days

Volume	Execution Focus	Lead	Primary Timing
V6 Technical Architecture	Common core, control/media plane, Kubernetes	Technology & Business Operations	Aug 2026–Sep 2027
V7 QA & Release	Independent QA, device/browser matrix, AI diagnostics	Technology & Business Operations	Aug 2026 onward
V8 Commercial	Free/Paid, pricing, payment, revenue, entitlements	Growth & Ecosystem	Sep 2026–Jun 2027; Day-90 minimum live
V9 Customer Success	Onboarding, support, health, VOC	Growth & Ecosystem	Oct 2026 onward; foundations in 90 days
V10 Security & Trust	TrustLock, privacy, security gates	Technology & Business Operations	Aug 2026 onward
V11 Ecosystem	Partners, resellers, country expansion	Growth & Ecosystem	Jan 2027–Jan 2028
V12 Executive Governance	Dashboards, completion scorecard, CEO oversight	CEO + Both Managers	Aug 2026 onward

Appendix C. Day-30 / Day-90 Readiness Gates

Day 30 — 8 September 2026

- PM Execution Control System operational and accepted.
- Core integrations materially working or on approved dated fallback plan.
- Konn3ct and 1Gov actively managed inside Odoo.
- Weekly outcome/evidence culture operating.
- CEO and manager dashboards live.
- QA records/evidence and customer portal operational.
- AI work-order/orchestration pilot established.
- Growth foundation: analytics, CRM, Free/Paid definition, landing/campaign prep and payment architecture materially ready.

Day 90 — 7 November 2026

- 10,000 qualifying Free Users and 300 qualifying Paid Users targeted and transparently reported.
- Stable-enough Konn3ct core with material user-experience improvement.
- Meaningful mobile reliability improvement.
- Payment/subscription/entitlement flow operating.
- Marketing and acquisition engine operating with attribution.
- Customer onboarding/support and feedback-to-engineering loop operating.
- QA/CI/CD/security gates active; Kubernetes foundation materially advanced.
- 1Gov protected and common-core convergence working.
- Internal execution capability measurably improved.
- Formal 90-Day Konn3ct Edge Execution & Growth Report approved.

Final Governing Principle

ONE BLUEPRINT • ONE CONNECTION FREEDOM DOCTRINE • ONE EXECUTION CONTROL SYSTEM • ONE COMMON CORE • THREE CONTROLLED DELIVERY TRACKS • ONE WEEKLY ACCOUNTABILITY RHYTHM • ONE EVIDENCE-BASED DEFINITION OF DONE • TRUSTLOCK™ BY DESIGN • AI-POWERED / HUMAN-GOVERNED
